



Republic of Turkey
Ministry of Environment, Urbanization and
Climate Change
General Directorate of Construction Affairs

**TÜRKİYE EARTHQUAKE RECOVERY AND
RECONSTRUCTION PROJECT
(TERRP)**

Subproject Name	Kahramanmaraş Province Afşin District Küçüktatlar Neighbourhood Rural Housing Project
Document Name	Environmental and Social Management Plan
Version	0.1
Delivery Date	08/05/2024
Approval Date	16/05/2024

Version /Date	Prepared by	Reviewed by
Version 0.0 04/03/2024	Fatma KULAKSIZ – Environmental Specialist Sibel OKDEMİR – Social Specialist Erdal YASA- Occupational Health and Safety Specialist	Emir Alp GÜNER – Project Director
Version 0.1 08/05/2024	Feray YOLOĞLU – Environmental Specialist Mustafa ERTEMİZ – Environmental Specialist Sibel OKDEMİR – Social Specialist Erdal YASA- Occupational Health and Safety Specialist	Emir Alp GÜNER – Project Director

This Environmental and Social Management Plan is developed by the Koltek Consulting Company within the scope of “Consultancy Services for Design Review and Reconstruction Supervision of Rural Housing (Ref: TERRP/CS-DESSUP-02)” under Türkiye Earthquake Recovery and Reconstruction Project.

INDEX

LİST OF ABBREVIATIONS.....	6
1. INTRODUCTION	7
2. THE RATIONALE OF THE ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN.....	8
3. LEGAL AND INSTITUTIONAL FRAMEWORK.....	9
4. PROJECT DESCRIPTION.....	10
4.1 Project Characteristics	13
4.2 Environmental and Social Baseline	13
5. INFORMATION ACTIVITIES AND PUBLIC PARTICIPATION FOR ESMP.....	16
6. ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN.....	17
7. REPORTING STRUCTURE	43
8 ANNEXES.....	44
Annex 1 Title Deeds	44
Annex 2: Photographs.....	45
Annex 3: Project Disclosure.....	49
Annex 4 Stakeholder Engagement Meeting Presentation.....	51
Annex 5 Stakeholder Engagement Meeting.....	56
Annex 6 Project Disclosure Materials	57
Annex 7 Neighborhood Settlement Plan (117/4 and 113/2 Parcels)	59
Annex 8: Screening Form (given as a separate document)	60

LIST OF TABLES

Table 1: Movable/Immoveable Assets Close to the Selected Parcel 113/2 and 117/4	13
Table 2: Environmental and Social Baseline.....	14
Table 3: Questions Posed and Answers in the Stakeholder Engagement Meetings.....	16
Table 4: Environmental and Social Management Plan	18

LIST OF FIGURES

Figure 1: Google Earth View of the Rural Housing Subproject Parcels 113/2 and 117/4.....	10
Figure 2: Satellite image of the selected subproject area (Parcels 113/2 and 117/4).....	11
Figure 3: Satellite general image for parcel 113/2 and 117/4.....	11
Figure 4: Area of Influence (AoI) 113/2 and 117/4 Parcels	12

LIST OF ABBREVIATIONS

AFAD	Disaster and Emergency Management Presidency
AoI	Area of Influence
WB	World Bank
C-ESMP	Contractor Environmental and Social Management Plan
DSI	State Hydraulic Works
E&S	Environmental and Social
ESHS	Environmental, Social, Health and Safety
ESMF	Environmental and Social Management Framework
ESMP	Environmental and Social Management Plan
ESS	Environmental and Social Standard
GBVH	Gender Based Violence and Harassment
GDCA	General Directorate of Construction Affairs
GRM	Grievance Redress Mechanism
Koltek	Koltek Consulting Company
LMP	Labor Management Procedure/Plan
MoEUCC	Ministry of Environment, Urbanization and Climate Change
OHS	Occupational Health and Safety
PIU	Project Implementation Unit
PPE	Personal Protective Equipment
SEA/SH	Sexual Exploitation and Abuse/Sexual Harassment
SEP	Stakeholder Engagement Plan
TERRP	Türkiye Earthquake Recovery and Reconstruction Project
TMP	Traffic Management Plan
WMP	Waste Management Plan
WWTP	Wastewater Treatment Plant

1. INTRODUCTION

The World Bank (WB) is supporting the Ministry of Environment, Urbanization and Climate Change (MoEUCC) in implementing the Türkiye Earthquake Recovery and Reconstruction Project (TERRP). WB finances TERRP activities under Component 3, Rural Housing Reconstruction and Recovery, and Component 4.3, Project Management, Monitoring and Evaluation. The general aim of TERRP is to provide access to municipal and health services as well as earthquake-resistant new rural housing in selected provinces affected by the February 2023 earthquake in Türkiye. The MoEUCC will be implementing the Project activities for Component 3; Rural Housing Reconstruction and Recovery, and Component 4.3; Project Management, Monitoring and Evaluation in close collaboration with the Disaster and Emergency Management Presidency (AFAD).

Under the scope of Component 3 Rural Housing Reconstruction and Improvement of TERRP, 29 houses in the Küçükatlar neighbourhood of Afşin District, Kahramanmaraş province, will be constructed in the new settlement area. 113/2 parcel and 117/4 parcel located in Küçükatlar Neighbourhood were identified as the sub-project areas. This Environmental and Social Management Plan (ESMP) is aimed at assessing and minimizing the potential negative environmental and social risks and impacts of the reconstruction of a total of 29 steel construction rural houses in this region. The destroyed or severely damaged houses and basic infrastructures in the selected neighbourhoods will be reconstructed in new settlement locations. Additionally, the measures to eliminate potential adverse environmental and social impacts during the projects, address health and safety measures details about stakeholder engagement activities, and the establishment of a Grievance Redress Mechanism (GRM) and outline the responsibilities of relevant parties within the project scope include in this Environmental and Social Management Plan.

2. THE RATIONALE OF THE ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN

Following the Environmental and Social Management Framework (ESMF) of the TERRP, the Project Implementation Unit (PIU) under the MoEUCC General Directorate of Construction Affairs (GDCA) has completed the Environmental and Social (E&S) Screening and the E&S Risk Rating was evaluated as “Moderate” based on the anticipated E&S risks and impacts. Referring to the ESMF, based on the E&S screening and subsequent assessment, a subproject based ESMP needed to be customized for the subproject namely Kahramanmaraş Afşin Küçüktatlar Rural Housing Project.

Consulting Company (Koltek) under its assignment “Consultancy Services for Design Review and Reconstruction Supervision of Rural Housing” with the name of the supervision consultant took the responsibility to customize the ESMP for the subproject. In the course of the customization, Koltek visited the subproject site before preparing ESMP having meetings with the contractor and Küçüktatlar Neighbourhood Mukhtar for an effective ESMP. Koltek has also used the ESMP format given in the ESMF Annex 4 as guidance.

It is the Contractor's responsibility to review, revise, and update the ESMP per its planning and decisions. This ESMP includes site-specific measures whereas developed limited to the available information. In the course of the planning and construction, there could be revisions in the methods of the construction due to feasibility and technical concerns. In such changes in the Contractor's way of construction, the ESMP shall be reviewed and revised by the Contractor and then submitted to Koltek for review. The Waste Management Plan, Pollution Prevention Plan, OHS Plan, Community Health, Safety and Traffic Management Plan, Water Supply and Wastewater Management Plan etc., will be prepared also by the Contractor and submitted to the PIU for approval by Koltek after including their review. The Contractor shall take due care to reflect the site conditions to the ESMP and require to be proactive in its planning and reflecting the revisions into this ESMP. The Contractor shall not start construction until all documents are approved by the PIU.

3. LEGAL AND INSTITUTIONAL FRAMEWORK

The legal and institutional framework for TERRP is comprehensively presented under Section 3 of the TERRP's ESMF. ESMF Section 3 indicates the legal framework of Türkiye followed by a brief explanation of the national environmental and social assessment regulatory process including permitting and defines gaps between the WB Environmental and Social Standards (ESS) and legislative requirements.

While developing the ESMP, both the ESSs and the legislative framework concerning the subproject-related activities are considered, and feasible and effective measures are recorded.

The ESMF for the Project (both English and Turkish) can be found at the following website:

English

https://webdosya.csb.gov.tr/db/kadiyap_en/menu

Turkish

<https://webdosya.csb.gov.tr/db/kadiyap/menu>

4. PROJECT DESCRIPTION

The destroyed and heavily damaged houses in the Küçüktatlar Neighbourhood of Afşin District of Kahramanmaraş will be rebuilt in the newly determined settlement area, a total of 29 rural houses are planned to be constructed within the scope of this part of the TERR Project. Besides, within the scope of the project, it is planned to build roads and pavements, install street lighting, establish a water network, and sewerage infrastructure, and build impermeable septic tanks. The new settlement area determined consists of two different parcels next to each other. For the Küçüktatlar sub-project, AFAD has allocated parcel 113/2, which belongs to the Ministry of Treasury and Finance, with a total area of 321,955.89 m², and parcel 117/4, which also belongs to the Ministry of Treasury and Finance, with a total area of 201,449 m². The total area of the two parcels is 523,405 square meters, and only 14% of this land, in other words, 72,637.91 m², will be used for the sub-project. 29 rural houses will be built on these parcels. The satellite view of the location is given below in Figure 1: **Google Earth View of the Rural Housing Subproject Parcels** 1, Figure 2 and Figure 3.

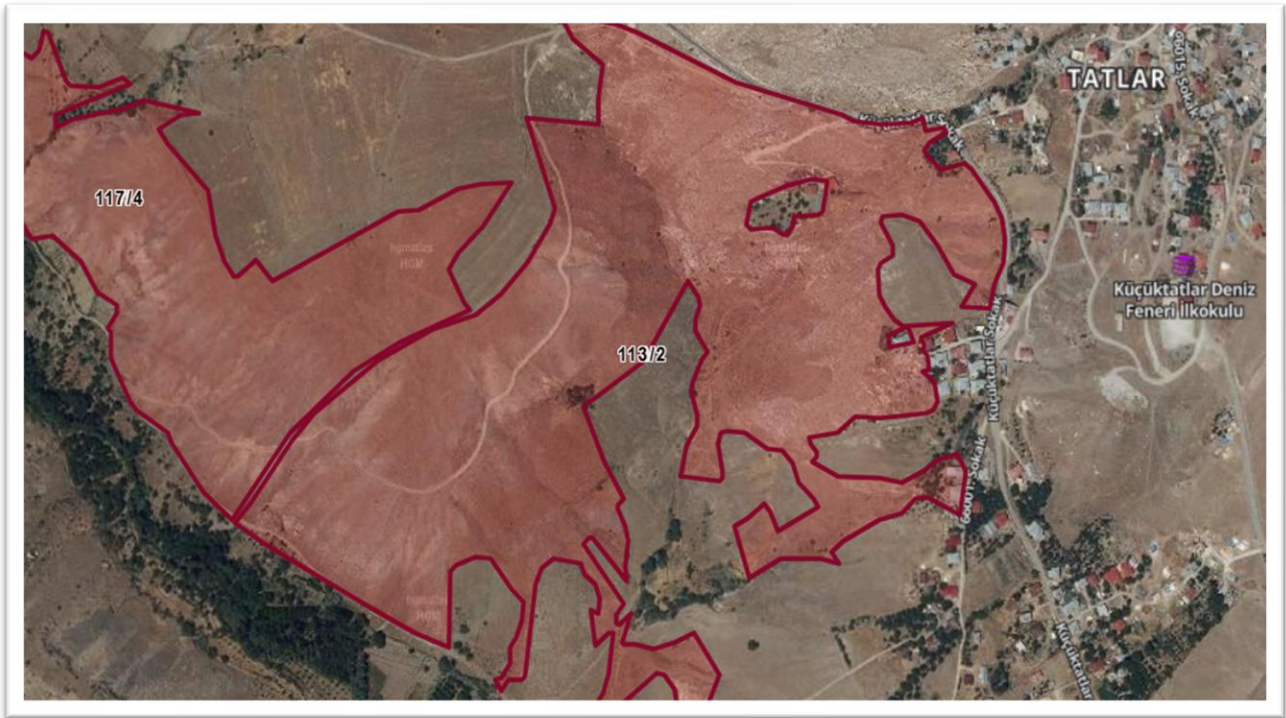


Figure 1: Google Earth View of the Rural Housing Subproject Parcels 113/2 and 117/4

The parcel and the construction site as well as the close dwellings and facilities are shown in

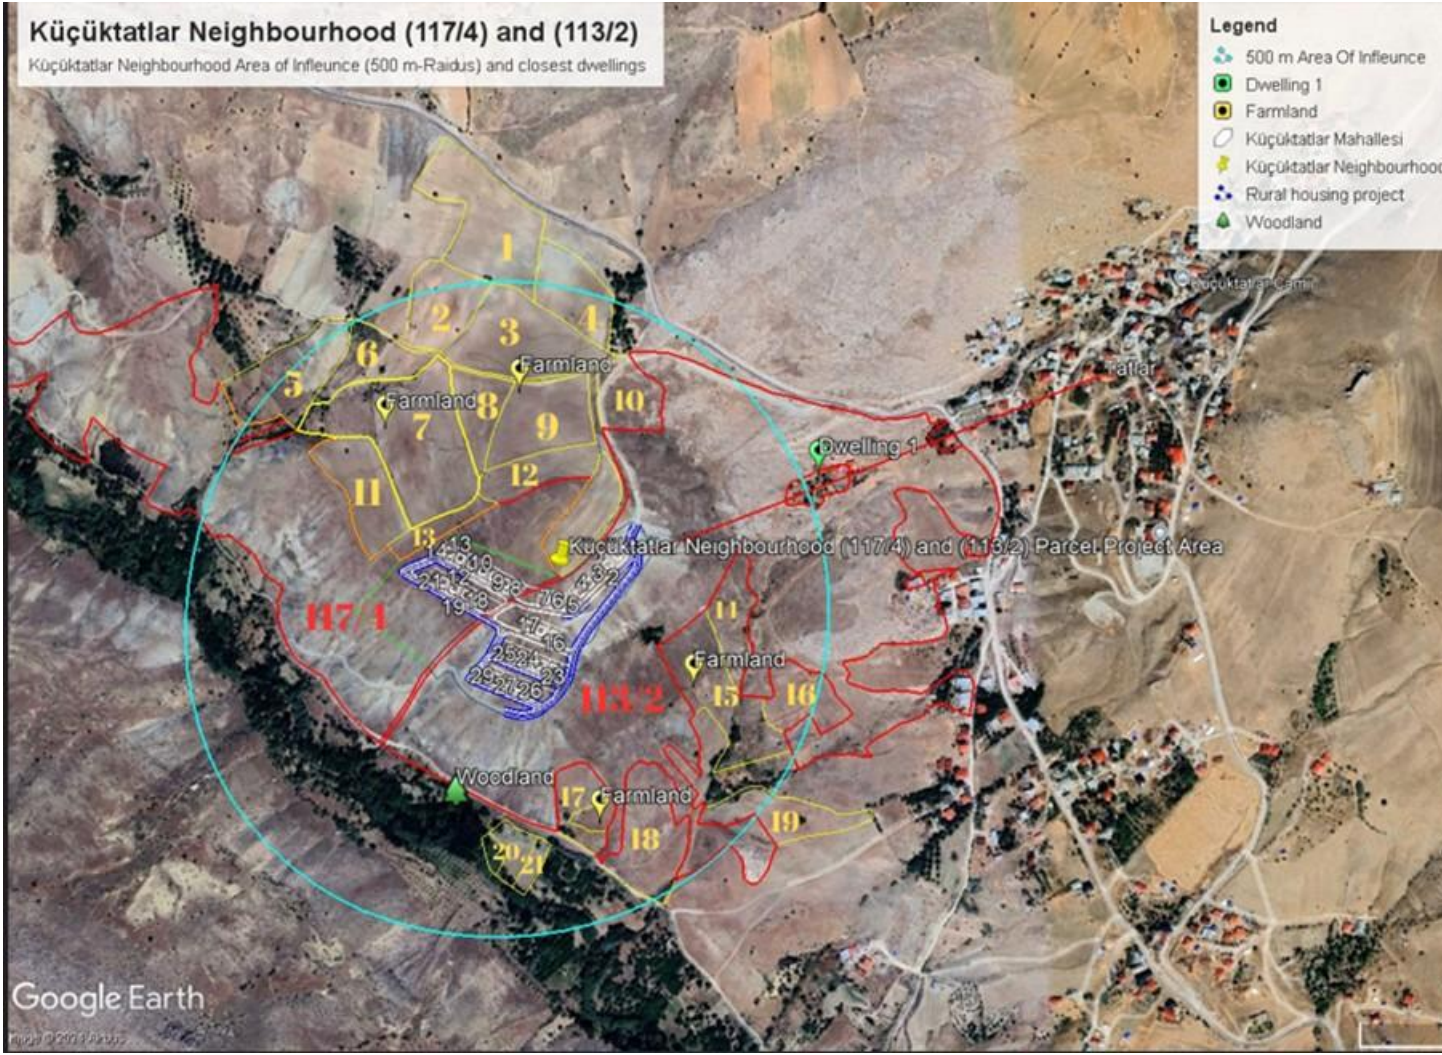


Figure 4: Area of Influence (AoI) 113/2 and 117/4 Parcels and Hata! Başvuru kaynağı bulunamadı. Table 1: Movable/Immoveable Assets Close to the Selected Parcel 113/2 and 117/4

and the distances to the close dwellings and other facilities and features are given in Table 1 and Hata! Başvuru kaynağı bulunamadı..



Figure 2: Satellite image of the selected subproject area (Parcels 113/2 and 117/4)



Figure 3: Satellite general image for parcel 113/2 and 117/4

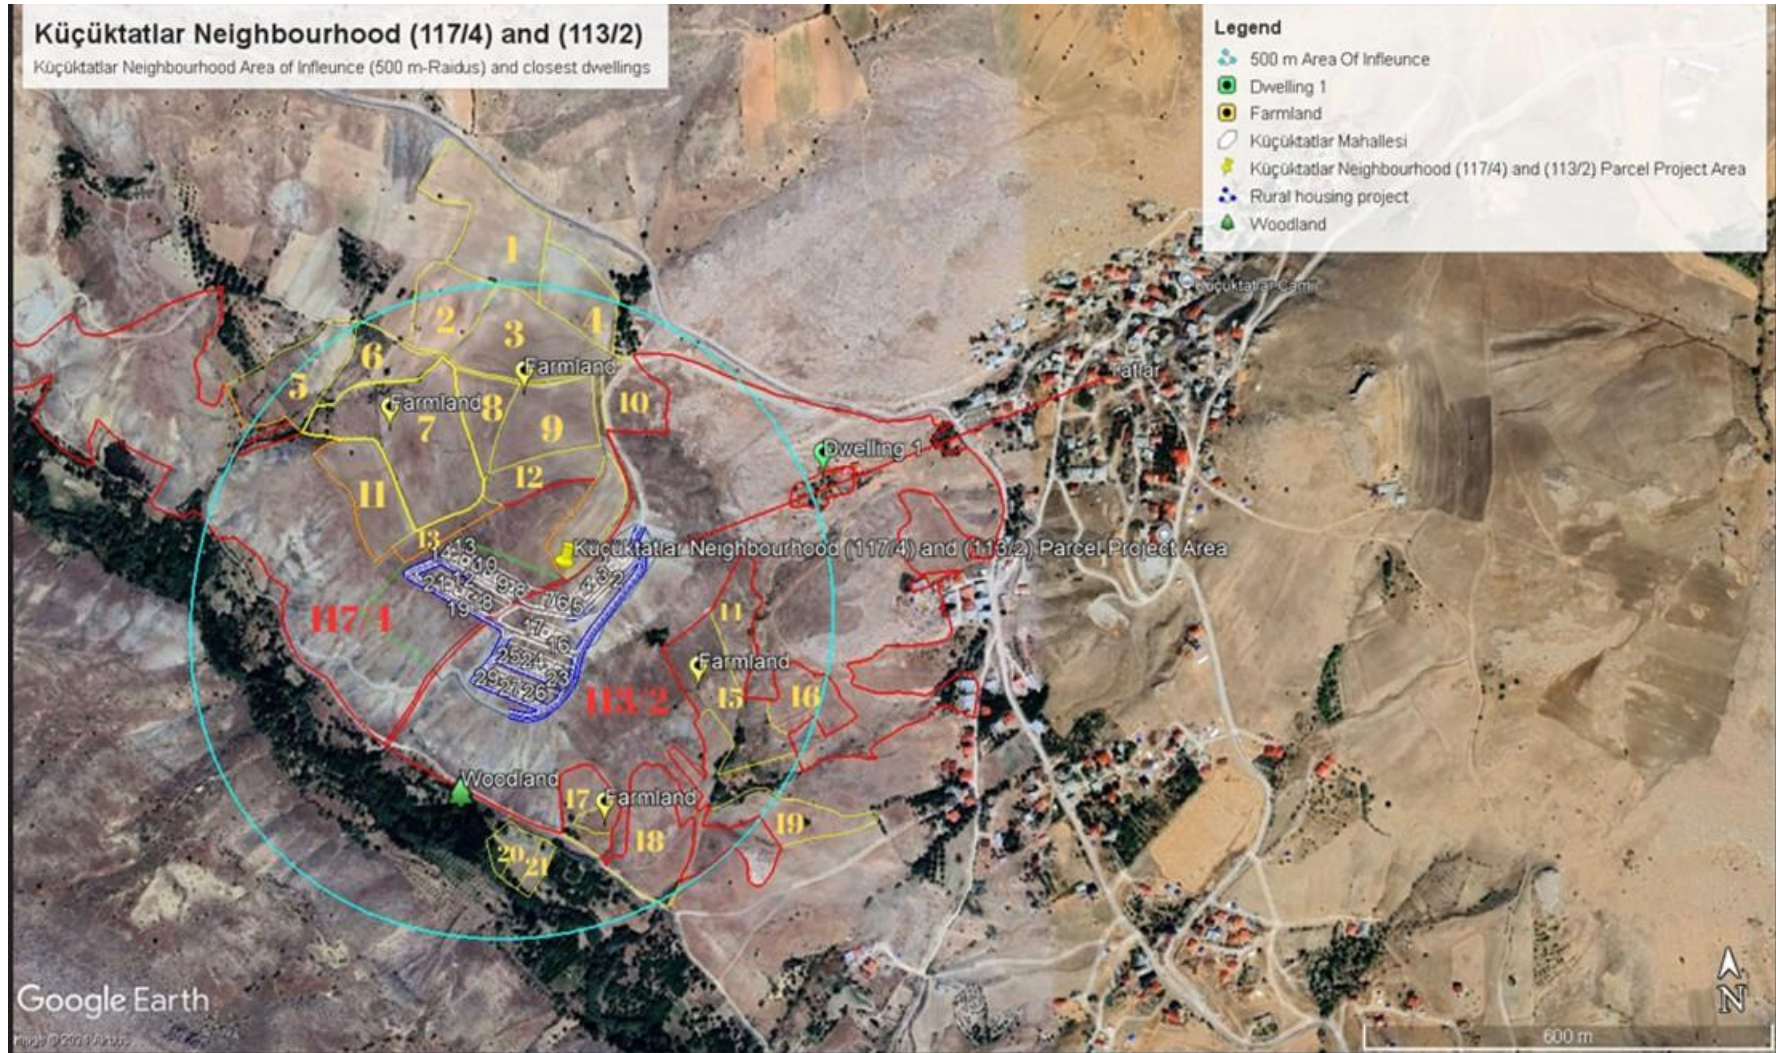


Figure 4: Area of Influence (AoI) 113/2 and 117/4 Parcels

Table 1: Movable/Immoveable Assets Close to the Selected Parcel 113/2 and 117/4

Dwelling / Facilities / Features	Air Distance (m)(*)
Dwelling-1-3	480 -500m
Stream	400 m
Farmlands (4)	60-160 m
Woodland	180 m
Neighbourhood center	750 m

(*) Figures indicate the distance from the boundaries of the selected area to the affected area

4.1 Project Characteristics

The features regarding the houses to be constructed and the awarded Contractor are listed as follows:

- Rural houses will be built on two different parcels that are next to each other. The total size of the allocated land is 523,405 m². 29 rural houses will be built using 72.637.91 m² of the allocated land. Rural houses are steel and designed with 3 bedrooms, 14.04 m² veranda. The duration of construction is 180 days.
- Settlement plans for each new location have been approved by MoEUCC; however, they might be revised, if deemed necessary.
- There will not be any construction of a concrete plant within the scope of the Project. The concrete needed for the construction of the rural houses will be procured from the nearest licensed facility.
- Wastewater will be collected in the impermeable septic tanks in both the work site and resettlement area.

4.2 Environmental and Social Baseline

The current environmental and social baseline conditions of the Küçükatlar Neighbourhood and the new location are summarized in **Hata! Başvuru kaynağı bulunamadı.** Table 2: Environmental and Social Baseline below. Here, the location of the neighbourhood and the transportation conditions to the new settlement area are explained in more detail:

The main sources of income in Küçükatlar is animal husbandry. Both selected areas are not used as pasture, animals are grazed on the plateau. There is a primary and secondary school in the neighbourhood with 150-160 students. There is a health center with a permanent nurse. There is a public hospital in the district center.

There is an asphalt road through Küçükatlar District. The distance of the project area to the residential area is 750 meters. There are sufficiently wide stabilized roads, field roads, etc. to be used during construction around the construction area. The area is located on the connection roads around the selected area and there is no transportation problem. There is a large amount of unused land suitable for use as a construction site inside and outside the site.

There is no source of water in the area of the rural housing project where both plot is to be built. There is a spring on the outside of the plot of 113/2 about 400 m away. A drinking water line passes 1 km away from parcel number 113/2. The drinking water line passes 1 km away from the selected area. There is a wastewater line within the neighbourhood, approximately 1 km away from the site. An energy transmission line passes 500-600 m away from the selected area. The measures to be taken in this context are defined in the Table 4 of this ESMP.

The south of the selected area 113/2 and 117/4 overlooks a deep valley (See: **Photo 2**, **Photo 3**, **Photo 4**). A stabilized road passes around the selected area and the road provides access to agricultural lands in the valley. There are settlements around this parcel, 480-500 m as the crow flies, and it is located approximately 750 m.

from the current neighbourhood centre.

Agricultural activities are carried out on neighboring parcels but there is no informal use for agricultural or pasture purposes in the selected areas.

It has been determined that the most sensitive receptors for both parcels are families living in the houses around the parcel. There are 3 houses and 4 agricultural lands in the nearest impact area of the parcels. It was determined that the natural sensitive receptors were a stream 400 meters away and a wooded area 180 meters away. Risks and mitigation measures related to dust, noise, public health and safety and traffic that may occur during construction are explained in the relevant columns of **Table 4** in this report.

On the selected areas the construction activities will not require the clearing of any trees. There is no vegetation, trees or shrub or forest that will lose its quality due to construction activities.

Selected parcels are not adjacent to a sensitive area (a historically, archaeologically or culturally protected area) or facility. There is an old castle (historical area) which is about 5 km and old Byzantine Bridge (historical area) approximately 3 km away from the plots of land.

The awarded contractor will perform land preparation and construction activities. The construction phase is anticipated as follows:

- a. Mobilization
- b. Grading for roads and road construction within the sub-project area
- c. Site inspections for geological assessment
- d. Grading and construction of houses and other units

This ESMP has been developed to encompass all environmental and social measures required during all sub-project activities. In case subcontractors are utilized by the contractor (for construction, concrete plant, catering services, security, etc.), it is the responsibility of the contractor to ensure that subcontractors operate in compliance with this ESMP, national regulations, World Bank ESSs, and World Bank Group General Environmental, Health, and Safety Guidelines. The contractor is obligated to monitor, report, record, and oversee subcontractors' work for quality performance.

Table 2: Environmental and Social Baseline

E&S Aspects	Küçüktatlar
Distance to the village/neighbourhood center	750 meter
Public facilities near (<0.5 km)	NA
Close dwellings	Please refer to Table 1
Other features	There are farm lands around the selected parcels
Sensitive Receptors	Farmers within the construction area, dwellings <0.5 km near to selected parcels, school children, residents of Küçüktatlar neighbourhood.
Land cover	Limestone and soil
Ownership	Ownership belongs to the State (Treasury)



E&S Aspects	Küçüktatlar
Presence of trees / Flora - Fauna	There is no vegetation, trees or shrub.
Presence of vulnerable/disadvantaged persons	There is one disabled person among the beneficiary. Some of the beneficiaries are elderlies over the age of 65.
Sexual Exploitation and Abuse / Sexual Harassment (SEA/SH) Risk (to be expected)	Yes, it is expected that some external labor will be hired for the sub-project site; therefore, there are some risks.

5. INFORMATION ACTIVITIES AND PUBLIC PARTICIPATION FOR ESMP


Afşin District, Küçüktatlar neighborhood stakeholder engagement meeting was held on September 30, 2024, at the study center in the condolence house in Küçüktatlar neighbourhood (**Annex 5 Stakeholder Engagement Meeting**). The meeting was planned to be held before the sub-project's rural housing construction started. However, one of the 2 separate parcels designated for a total of 29 houses (108/1) was not accepted by the rights holders due to its distance from the demolished settlement and the high and sloping terrain, and they stated that they did not want to reside there when the houses were completed. Upon this, in addition to the 113/2 parcel, the 117/4 parcel was allocated and it was decided to build a total of 29 houses on both parcels, and the parcel No. 108/1 was cancelled.

In order to provide accurate and final information to the right holders, it was deemed appropriate by the Consultant company and PUB not to hold a stakeholder participation meeting until the situation was clarified. However, during the approval process of the plans, housing construction was also started in order to benefit from the suitable seasonal conditions and not to delay delivery, and significant progress was made.

After the date of the meeting was determined, the ESMP prepared for this sub-project was presented to the public in hard copy at the head office and in the village market where the complaint box is located as of October 20, 2024 (**Hata! Başvuru kaynağı bulunamadı.** The announcement of the meeting was made by mukhtar from the neighborhood mosque and through face-to-face meetings. A total of 10 people from the right holders, including 10 men and 3 women, attended the meeting. Some of the rights holders live in the village settlement affected by the earthquake, some in nearby urban centers. For this reason, not all rights holders could attend the meeting.

The meeting was attended by the MoEUCC 2 PUB experts, the social, environmental and OHS experts of the Koltek Consulting, the mechanical engineer and the assistant project manager. The site control manager, civil engineer, OHS expert from the field team of Koltek, as well as the construction site manager of the contractor firm also attended the meeting. Two project experts from the Koltek office also attended the meeting via online.

The meeting started with the introduction of the project by the MoEUCC social expert. The power point presentation (**Annex 4 Stakeholder Engagement Meeting Presentation**



prepared specifically for the sub-project was made by the social, environmental and OHS experts of Koltek. In the presentation; the social and environmental impacts of the project and mitigation measures, project documents, management plans, grievance redress mechanism and communication channels were explained. The brochures prepared for the sub-project were distributed to the participants and the poster was placed on the complaint box (**Annex 6 Project Disclosure Materials**

At the end of the meeting, 8 people responded to the participant satisfaction survey. The survey results will be analyzed and reported and submitted to the PUB as a separate document. After the presentation, participants were asked if they had any questions and the questions were answered by the experts. The questions and answers are presented in the Table-2 below.

Table 3: Questions Posed and Answers in the Stakeholder Engagement Meetings

Querist	Respondent	Question Raised	Answer Given
---------	------------	-----------------	--------------

Village Resident	Contractor's Project Manager	"When will the construction of the houses will be started? Everyone is staying in containers, we have no electricity or water.". We will probably start construction within 10 days."	"The approval process for the land takes some time. We have set up our construction site"
Village Resident	Contractor's Project Manager	"When can our houses be completed? Is that possible this year?"	"It is very difficult to finish this year. We can deliver them after winter and at the beginning of summer"

6. ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN

The table below represents the customized Environmental and Social Management Plan (ESMP), outlining the necessary measures for the Contractor to adhere to during the sub-project activities. This plan encompasses anticipated environmental and social risks and effects specific to the sub-project, along with recommended mitigation measures. It details the stages where these risks/effects are expected to occur, indicators within the monitoring system, frequency, responsibilities, and estimated costs. This ESMP comprehensively defines the strategies to address these risks/effects throughout the project timeline.

The implementation of the specified measures, the Contractor's execution system, the Contractor's organizational structure, site-specific E&S management plans, their effectiveness, and the monitoring plan to be implemented by the Contractor will be monitored by Koltek. The Contractor will be subject to oversight to establish an effective system for managing and monitoring E&S matters related to sub-project activities. Besides, the Contractor shall be reviewed the ESMP prepared by the Consultant and commit to implement the ESMP or prepare the Contractor's ESMP (C-ESMP) if needed. The contractor shall also prepare sub-management plans, e.g. Waste Management Plan, Pollution Prevention Plan, OHS Plan and Community Health, Safety and Traffic Mangement Plan, etc. and submit them to the consultant for review. The consultant in turn will send these documents with his/her comments to the PIU for approval.

Table 4: Environmental and Social Management Plan

Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
General for All Construction Works										
Environmental and Social (E&S) Management: Inadequate management of the environmental and social risks and impacts of the subproject	<p>The Contractor's Environmental and Social Management Plan (C-ESMP) will be prepared, submitted for approval, and then implemented. C-ESMP will be submitted before the commencement of construction works, and no construction activity will take place within the scope of the sub-project until the C-ESMP is approved. The C-ESMP will include, at least the following site-specific management plans:</p> <ul style="list-style-type: none"> Occupational Health and Safety (OHS) Plan including risk assessment report and emergency response plan (Refer to the draft in TERRP ESMF Annex-10) Community Health, Safety and Traffic Management Plan (Refer to the outlines in TERRP ESMF Annex-11) Hazardous Material Management Plan, if needed Waste Management Plan (Refer to TERRP ESMF Annex-8) Pollution Prevention Plan (Refer to the outlines in TERRP ESMF Annex-12) Water Supply and Wastewater Management Plan Labour Management Plan (LMP) (To be prepared in accordance with TERRP's LMP) 	X	X		All site-specific management plans are approved prior to construction and implemented throughout the construction period. Monthly E&S Progress Report		X		Contractor (implementation) Supervision Consultant (audit) and Report Preparation	Within the cost of construction
	At least a full-time A/B class OHS specialist and a full-time environmental specialist are employed before starting construction work. The contractor is obliged to obtain approval by submitting resumes of specialists. It is imperative that these specialists are present on-site during the construction period.	X	X		Relevant E&S personnel are provided and maintained throughout the construction period.		X		Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	A training program is prepared by the Contractor and all employees are trained on the main environmental, social, health and safety (ESSG) risks and workers' responsibilities associated with such construction works before they start working on site. The training program is repeated monthly. The Contractor's monthly training program also covers issues related to the Code of Conduct, such as sexual harassment, sexual and/or gender-based violence, especially against women and children, and respectful attitude in interacting with the local community.	X	X		Environmental and social training program is approved and implemented according to schedule and documented. GBVH training program is implemented and documented		X		Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
	All necessary permits (Land Use Permit, Waste Disposal Permit / Protocol from the Municipality, Environmental Permit, Water Use Permit from the State Hydraulic Works, Electricity Connection and Use Permit, Excavation waste disposal protocols with Municipalities, etc.) will be obtained and the installation of facilities will be ensured prior to construction.	X			Permissions and relevant official letter	X			Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
	<p>During the dry season, dust in exposed work areas will be minimized by regularly spraying the ground with water.</p> <p>Construction debris will be kept in a controlled area and sprayed with water to reduce dust.</p> <p>The surrounding environment such as roads, etc. will be kept free of debris to minimize dust.</p> <p>Aggregate materials will be kept covered to prevent fine soil particles from being suspended or dispersed in the air as a result of wind blowing or dispersing by stray animals.</p> <p>In the case of pneumatic drilling during excavation, the dust will be suppressed by continuous water spraying and/or construction dust curtain housings on site if required. Its paths will be cleared of excavation to minimize dust.</p> <p>Where stabilized roads are used, they will be reinforced with a</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
<p>Air quality: Dust generation around the sub-project site due to construction activities and emissions from construction equipment and vehicles</p>	<p>stabilizing layer where necessary. Open burning of construction/waste materials on site will be avoided. The operating hours of generators/machines/equipment/vehicles will be appropriately reduced. The traffic routes to be used in the Traffic Management Plan are shown and drivers and operators will be trained accordingly. Vehicles shall not be loaded beyond their capacity. Vehicles will be kept within the area. New and well-maintained vehicles will be used to control gas emissions that will occur within the scope of the activity. All vehicles and all work machines to be used will have exhaust emission permits and all vehicles will be regularly maintained or inspected. Unnecessary use of machinery and equipment that causes emissions is prevented. Trucks carrying materials will be covered to reduce dust emissions. When passing through public areas is unavoidable, vehicle speed will be kept under control to minimize dust distribution resulting from vehicle transportation. While the speed limit in the project area is 30 km/h, it will be 50 km/h in the city. Tires of trucks operating in the construction site will be washed before leaving the area (street). In case of grievances about dust formation from nearby devices, 24-hour dust measurements are performed by an authorized laboratory. If the measured levels are above limit values, mitigating measures will be developed in this context; For example, wetting/irrigation activities are increased, non-toxic chemicals will be applied, and the speed of vehicles will be controlled.</p>		X		<p>Visual inspection of air quality control measures</p> <p>Records of maintenance Records of complaints</p>	X			<p>Contractor (implementation) Supervision Consultant (audit)</p>	<p>Within the cost of construction</p>



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
<p>Noise: Noise generation from construction vehicles and equipment</p>	<p>Construction will be limited to certain deadlines defined in national legislation, and activities will be planned in consultation with nearby communities. Thus, the noisiest activities will be carried out during periods that cause the least disturbance.</p> <p>During operation, the engine covers of generators, air compressors and other electrical-mechanical equipment will be closed.</p> <p>Equipment will be placed as far away from residential/community areas as possible.</p> <p>Maintenance procedures ensure that all equipment and machinery are in good working order, and acoustic enclosures will be placed around generators to reduce noise levels.</p> <p>Noise control methods such as fences, barriers or deflectors (such as muffling devices for combustion engines or planting fast-growing trees) will be used when possible.</p> <p>Unnecessary use of alarms, horns and sirens will be avoided.</p> <p>Project-related transportation through public areas will be minimized.</p> <p>The area of Küçükatlar, where the construction and operations will take place on selected plots is 750 meter away from the village settlement. That is why no adverse noise effect is expected during the construction. In cases where traffic needs to be limited in residential areas at night; traffic flow is ensured only through designated routes, and in case of night work, the necessary permits will be ensured. However, the Contractor will avoid night work as much as possible and will complete its work during the day.</p> <p>All employees will be trained to follow precautions and best practices. In case of complaints about noise from the nearest receptors, noise measurements will be made by the authorized laboratory. If the measured levels are above the limit values, mitigation measures will be developed in this context; For example, acoustic barriers will be installed for mechanical equipment, working hours will be limited for certain pieces of equipment or</p>									
			X		<p>Visual inspection of noise control measures</p> <p>Equipment and machinery maintenance records</p> <p>Complaint records</p> <p>Measurement results</p>		X		<p>Contractor (implementation)</p> <p>Supervision Consultant (audit)</p>	<p>Within the cost of construction</p>



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	operations, etc.									
Occupational Health and Safety: OHS-related risks arising from unsafe practices and hazards such as working at height, rotating and moving equipment, electrical safety, working with hazardous substances, etc.	When planning activities, the following steps will be considered with OHS specialist to avoid people getting injured: the hazards associated with construction activities and how they can be avoided, The skills of the personnel involved and their suitability to carry out the work adequately, the use of work equipment and machinery and their adequacy to eliminate the risks associated with the work, electrical safety will be taken into account by evaluating other risks High-risk activities will be avoided as much as possible, and the control hierarchy method will be used for identified risks. A proper risk assessment is prepared before construction work begins and appropriate measures will be provided to avoid risk and, if avoidance is not possible, adequate measures to minimize risk. An OHS Plan will be developed that reflects the risk assessment inputs and outputs, including the Root Cause Analysis, and the risk assessment tracking systems developed.	X			Meeting minutes Risk assessment		X		Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
	Appropriate signage will be placed at construction sites to inform workers of the ground rules and regulations they must follow.									
	A short weekly Toolbox talk will be given to the construction workers by the contractor's OHS specialist about the ESSG risks associated with the construction activity to be carried out.									
	A safe working environment will be provided for workers.									
	Personal protective equipment (PPE) (hard hats, gloves, dust masks, goggles, full body safety harnesses and safety boots, etc.) in accordance with international best practices and Turkish Legislation will be provided before construction activities.									
All activities will be carried out in accordance with the Occupational Health and Safety Law (Official Gazette dated 30 June 2012 and		X			Visual inspection of control measures Training records OHS records Employee records Incident/accident statistics and records Records of workers' complaints	X			Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>numbered 28339) and related regulations, as well as the World Bank Group EHS Guidelines.</p> <p>Any serious incidents that may have significant adverse effects on the environment, affected communities, the public or workers will be immediately reported to the MoEUCC PIU (through supervisory consultants). The MoEUCC then reports any serious incident to the WB within 48 hours, and an incident investigation report will be sent to the WB within 30 days, along with a root cause analysis and corrective action plan.</p> <p>The work site will be kept clean and free of unnecessary material on a daily basis. A first aid kit with bandages, antibiotic creams, etc., or medical facilities will be provided.</p> <p>Safety guidelines for the storage, handling, and distribution of hazardous materials will be followed to minimize the possibility of misuse, spillage, and accidental exposure to people. A defined hazardous material storage area will be created, which has a ventilation arrangement, where there is a collection channel with a closed and spilled well for the collection of spilled material, where all materials will be stored according to the requirements in the safety data sheets.</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>Corrosive liquids and other toxic materials will be stored in properly sealed containers for collection and disposal in properly secured areas.</p> <p>It will be ensured that the structural openings are adequately sealed/protected. Loose or light materials stored on roofs or open floors will be fixed. Hoses, power cords, welding cables, etc., will be prevented from being found in heavily used walkways or areas. During heavy rains or any emergency, all work will be suspended.</p> <p>The following precautions will be applied in constructions that require working at height:</p> <ul style="list-style-type: none"> ▪ Work will be done from as many workplaces as possible. ▪ Individuals with the following personal risks will not be permitted to work at heights: vision/balance issues; certain chronic diseases like osteoporosis, diabetes, arthritis, or Parkinson's; individuals taking specific medications such as sleeping pills, tranquilizers, blood pressure medications, or antidepressants; those who will be experienced recent falls or similar incidents within the last 12 months. ▪ Only individuals with adequate skills, knowledge, and experience will be allowed to perform the task. ▪ The safety of the location where work at heights will be conducted (e.g., a roof) is checked for its safety. ▪ Precautions will be taken when working on or near fragile surfaces. ▪ Safety measures against falls, such as safety belts and simple scaffolding/railing, will be provided for work at heights. <p>Oil, grease, paint and dirt will be immediately removed to prevent slipping.</p> <p>Trained operators will be employed to operate special vehicles such as forklifts safely, including safe loading and unloading.</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>Moving equipment with limited rear visibility is equipped with audible backup alarms.</p> <p>Flaggers will be provided to each moving equipment operator to guide the movement of equipment.</p> <p>Before construction activities, all open electrical appliances and lines will be marked with warning signs.</p> <p>All electrical cords, cables and power tools will be checked for frayed or unwound cords and the manufacturer's recommendations will be followed for the maximum permissible operating voltage of portable tools. There will be a leakage current relay in electrical panels.</p> <p>Incidents, including near misses (major incidents including fatalities, lost-time incidents, spills, fires, etc.) and trainings are recorded.</p> <p>Necessary precautions will be taken against the occurrence of fire and a sufficient number of firefighting equipment will be provided for the office, camp area and site.</p>									
<p>Health and safety:</p> <p>Community health and safety risks associated with construction activities, including traffic and road-related risks (such as risks to the population due to inadequate construction and traffic management) arising from increased traffic volumes and the movement of heavy vehicles</p>	<p>Since the subproject is a construction project, people living around the construction area, people living in the existing residential area (due to the material transportation), the agricultural lands and the farmers in the surroundings and within the project area and domestic animals around the transportation roads can be considered the sensitive receptors. The mitigation measures to be taken in the Community Health, Safety and Traffic Management Plan including the Traffic Management Plan will be determined respecting these sensitive receptors.</p> <p>To prevent public access to the construction site, it will be surrounded by a fence. Material stocks/storage areas will be kept away from the public and surrounding living areas.</p> <p>Children are kept away from the construction area. It will be ensured by security guards, fences around the site and warning signs.</p> <p>The route of construction vehicles will be arranged in a way that does</p>		X		<p>Visual inspection of control measures</p> <p>Traffic accident records</p> <p>Complaint records</p>	X		<p>Contractor (implementation)</p> <p>Supervision Consultant (audit) PIU</p>	<p>Within the cost of construction</p>	



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>not prevent public access to agricultural lands and gardens located near or adjacent to the construction site, and security measures are taken.</p> <p>All earthen waste pits are filled after construction will be completed to prevent stagnant water, waterborne diseases and possible drowning.</p> <p>The driving speed of vehicles will be controlled, especially when passing through public places, nearby schools, health centers or other sensitive areas.</p> <p>If there are school children nearby, traffic safety personnel will be assigned to direct traffic during school hours, if necessary.</p> <p>During the night, the sub-project area is illuminated.</p> <p>The construction site and its surroundings will be kept clean. It will be ensured that broken windows are cleaned immediately to prevent fire.</p> <p>Safety guidelines for transporting hazardous materials to the site will be followed, aiming to minimize the potential for spills and accidental exposure of people due to traffic accidents.</p> <p>All drivers undergo safety and environmental and social awareness training; driving performance will be assessed and monitored with additional training provided if necessary.</p> <p>Driver training includes advice on behaviours to reduce the potential for disturbance, including the use of horns, loud radios with windows open, switching engines off when not in use, strictly observing speed limits and not accelerating or braking aggressively. A telephone number where the public can complain is displayed on the contractors' work vehicles.</p> <p>It is ensured that the daily life of the people living in the surrounding places of the construction site will be not affected, and transportation does not become difficult.</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>In case of damage to the roads caused by vehicles passing through the settlement during material transportation, the Contractor undertakes to cover the damage the roads will be repaired immediately by the Contractor.</p> <p>Vehicles will be regularly maintained to minimize potential serious accidents due to equipment failure.</p> <p>In areas accessible to all stakeholders (including construction sites), information on issues related to labor flow and measures taken against infectious diseases that may occur after the disaster (e.g. COVID-19 virus) is made through appropriate communication tools (e.g. online/visual materials and verbally).</p> <p>In the event of the occurrence of any epidemic or pandemic/infectious disease, including COVID-19, the Ministry of Health, the Ministry of Family and Social Services, and the Ministry of Labour and Social Security will prepare the guidance and guidelines to will be prepared by the World Health Organization.</p> <p>Ensure that the construction site will be appropriately secured, and construction-related traffic will be appropriately regulated (including proper route planning). These measures will include, but are not limited to:</p> <ul style="list-style-type: none"> • Direction signs, warnings, barriers, and traffic guidance: The site will be visible, and the public will be alerted to all potential hazards. • Specifically, traffic management systems and personnel training for site access and heavy traffic near the site. Ensuring safe crossings and passages for pedestrians in areas obstructed by construction traffic. • Adjusting working hours according to local traffic regulations, e.g., avoiding heavy transportation activities during peak hours or times of animal movement. • Traffic signs and measures will be designed and placed for 									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>vulnerable people sensitive (physically disabled, elderly, illiterate, women, children, students, etc.). They will be easily understandable and markable by the vulnerable.</p> <ul style="list-style-type: none"> Warning signs will be placed for domestic animals such as chickens, goats and sheep that may enter the roads while passing through residential areas. 									
<p>Land Acquisition and Resettlement: Involuntary land acquisition, including impacts on livelihoods, and relocation of community members (if necessary) to new settlement areas</p>	<p>Since there is no land subject to expropriation and/or easement rights for the sub-project, there is no need to prepare a Resettlement Action Plan (RAP).</p> <p>During construction activities, if any damage occurs to third-party assets, lands, crops, vineyards etc., the Contractor will compensate the damage according to WB ESS5 requirements, based on the "full replacement cost."</p> <p>Stakeholder categories, including sensitive groups, will be identified, and consultations will be held regarding the Project with these stakeholders. Project-level Stakeholder Engagement Plan (SEP) will be implemented.</p> <p>Topsoil will be stripped and stored in designated areas. When storing topsoil, it should be stored at a maximum height of 3 m and the incline of slope should not exceed 30 degrees. The slope is lightly compressed with the work machine bucket.</p> <p>It is ensured that the area to be stored does not have a slope of more than 5%. Excavation and backfilling of the subsoil may be involved in land levelling and landscaping operations. There will be no storage of excavation-related excavation in the area, all of it will be used for backfilling for levelling.</p> <p>Entrances to neighbouring lands outside the project area will be blocked, thus preventing any impact on neighbouring parcels.</p> <p>Measures will be taken to ensure that farmers engaged in agricultural activities near the construction site continue their activities and that livelihood impacts are prevented. These measures will also be permanent after the construction is</p>	X	X	X	Complaint records Survey Reports	X	X	Contractor (implementation) Supervision Consultant (audit) PIU	Within the cost of construction	



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>completed.</p> <p>Measures will be taken not to prevent access to the lands of farmers and to mitigate possible dust and traffic impacts.</p> <p>It is ensured that excavation material is not mixed with topsoil.</p>									
<p>Water Quality and Wastewater: Water pollution in nearby surface waters due to wastewater/wastes generated in the construction area due to construction activities</p>	<p>To prevent sediment from moving outside the site and flowing into adjacent roads and lands, erosion and sediment control are established using, for example, straw bales and/or silt fences.</p> <p>Efforts are made to minimize the storage or disposal of wastewater on-site.</p> <p>To prevent potential adverse effects on surface waters, temporary or final waste disposal or discharge into or near surface waters will be avoided. No polluted materials, solid waste, toxic or hazardous substances will be stored, poured, or disposed of in water bodies for dilution or disposal purposes.</p> <p>Construction vehicles and machinery (if applicable) will be washed only in designated areas where it will be determined that the rinse water will not contaminate natural surface waters.</p> <p>The wastewater generated by workers on the construction site will be deposited in the septic tank that will be impervious, in accordance with “Regulation on Pit Opening Where Sewer System Construction is not Applicable” published in Official Gazette No: 13783 dated 19.03.1971. Temporary toilets with septic tanks can also be used for this purpose. Septic tank wastewater is periodically removed by vacuum trucks and disposed of in accordance with a protocol established with the relevant municipality that has a licensed wastewater treatment plant (WWTP). The protocol will be submitted to the PIU.</p> <p>There is no drinking water network to the selected areas. However, there is drinking water pipeline 1 km. away from the 113/2 parcel. It will be planned to use this network to supply drinking water to Küçüktaşlar subproject area. There will not have sewerage network in the project areas. Therefore, the wastewater will be</p>		X		<p>Visual inspection of control measures</p> <p>Septic tank wastewater disposal records (if applicable)</p> <p>Wastewater quality measurement records (if applicable)</p> <p>Complaint records</p>	X			<p>Contractor (implementation) Supervision Consultant (audit) PIU</p>	<p>Within the cost of construction</p>



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>collected in the septic tank by constructing a sewerage network on the site.</p> <p>Throughout the project phases, records will be kept regarding the extraction of domestic wastewater by sewage truck.</p> <p>Invoices/receipts for each transportation/disposal will be collected and archived.</p> <p>Natural water flow will not be obstructed or diverted to prevent riverbeds from drying out or residential areas from being submerged.</p> <p>The flow of natural waters will not be obstructed or diverted in another direction, which may not lead to the drying up of river beds or flooding of settlements.</p> <p>Necessary permits are obtained from authorized bodies for the use of any natural water source.</p>									
Soil and Groundwater Quality: Soil and groundwater contamination due to accidental spills and soil erosion as a result of improper waste management	<p>For proper waste management, mitigation measures specified in the "Solid and Hazardous Waste" section below will be applied.</p> <p>The remaining concrete or syrup in concrete mixers will not be poured onto the construction site, its surroundings or access roads of the construction sites. Drivers and operators will be trained accordingly.</p> <p>Hazardous materials, including chemicals, will be collected and secured in a designated storage area to prevent spillage and overturning.</p> <p>The lids of containers containing semi-used chemicals shall be kept closed when not in use. Intervention methods for spillage will be implemented to limit the exposed area in case of any spillage of hazardous substances or hazardous waste. Project employees will be trained in spill response measures.</p> <p>Appropriate spill kits will be placed in suitable locations on the construction site.</p> <p>Construction will be appropriately planned during the dry season.</p>		X		<p>Visual inspection of control measures</p> <p>Incident records</p> <p>Topsoil stripping records</p> <p>Training Records</p> <p>Complaint records</p>	X		Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction	



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>The length and steepness of slopes will be limited and minimized. Upon completion of work, reclamation areas will be covered with topsoil and promptly re-vegetated with fast-growing plants (grass, shrubs, and trees).</p> <p>Topsoil up to a depth of 10 cm will be stripped and stored for reclamation works in permitted areas such as parking lots, and social facility areas within the sub-project site until construction is completed. It will be stockpiled in a herringbone pattern up to a maximum height of 2 meters and lightly compacted at the edges to prevent rainwater ingress. Ditches will be created around stockpile heaps to collect surface runoff and discharge it to the environment. Excess excavation materials, if any, will be stored in designated areas within the permitted area of the sub-project site and transported to land approved by the Municipality. Written permission is obtained from the Municipality for the transportation of excess excavation materials.</p> <p>The personnel and those concerned are warned that it is forbidden to dump the domestic solid wastes that will be generated within the scope of the activity in question into underground and surface waters, lakes and streams, similar receiving environments, streets, roads and open areas, and the necessary trainings are provided.</p>									
	<p>Wastes will be managed in accordance with the waste management hierarchy (prevent, reduce, reuse, recycle, recover, dispose), and personnel will be trained in waste management.</p> <p>Wastes will be separated as recyclable, hazardous, and non-hazardous waste. General construction waste, organic, liquid, and chemical wastes will be segregated on-site and stored in appropriate containers. Non-hazardous wastes, inert and biologically degradable wastes, and recyclable wastes must be collected separately, ensuring that hazardous wastes are not mixed with other waste types.</p> <p>Wastes will be disposed of at licensed disposal sites/facilities</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
Solid and Hazardous Wastes: EHS risks due to improper management of waste from construction activities (construction demolition waste, hazardous waste, biodegradable waste, recyclable waste, non-hazardous waste, etc.)	<p>(excavation waste storage areas, landfill sites, recycling/recovery facilities, etc.). Disposal of waste will be recorded in a tracking schedule and permits/licenses of disposal facilities will be obtained.</p> <p>A temporary waste storage area, equipped with a suitable drainage system, appropriate spill kits, and firefighting equipment, will be established on impermeable ground, and covered with a roof within the construction area. Wastes will be temporarily stored in separate compartments (labelled with waste codes) to prevent them from reacting with each other. Hazardous wastes will be stored in the temporary waste storage area for a maximum of six (6) months, while non-hazardous wastes will be stored for a maximum of one year. If a thousand kilograms or more of hazardous waste is produced monthly, a temporary storage permit must be obtained from the Provincial Directorate of Environment and Urbanization.</p> <p>Excavation materials will be utilized for backfilling and recovery purposes wherever possible, and other suitable reuse options will be evaluated. Licensed transport vehicles to licensed excavation waste storage areas determined by the district/region's relevant authorities will separately transport excess excavation waste. The respective municipality under the established protocol will collect household solid wastes. Hazardous wastes will be transferred to licensed waste disposal facilities via licensed waste transport companies, while recyclable wastes will be transferred to the relevant licensed recycling/recovery facilities. All protocols will be submitted to the PIU</p> <p>Personnel are assigned for spill response; these personnel will be trained and ensure that they are ready for immediate intervention in case of leakage. In order to provide timely and adequate intervention, leakage and spill response equipment will be kept ready and this equipment is ensured to be available for immediate intervention in the work area with all kinds of chemicals.</p>		X		<p>Visual inspection of control measures</p> <p>Waste production and disposal records</p> <p>Official correspondence with the municipality</p> <p>Training records</p> <p>Complaint records</p>	X			Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>If necessary, absorbent pads or materials will be used on storage floors. Absorbent pads or materials will be kept ready in chemical material storage areas, waste storage areas, and fields for immediate use when necessary.</p> <p>For domestic and recyclable waste; separate waste containers will be provided (leak-proof garbage containers for domestic solid waste, waste bins for packaging waste, and containers according to the type of recyclable waste in the temporary waste storage area). The type of waste to be collected in the waste bins will be written on the bins.</p> <p>Employees will be trained on the management of non-hazardous waste management and the use of separate waste containers.</p> <p>If waste batteries are generated within the scope of the activity in question, they will be collected in the waste battery collection box in the administrative offices of the project area, separately from other wastes, and delivered to collection points established by businesses or municipalities that distribute</p> <p>Within the scope of the work, maintenance and tire changes of the vehicles will be carried out by the relevant services, but in the case of end-of-life tires in the field of activity, they will be first collected temporarily in the temporary waste storage area to be created and then delivered to licensed companies.</p> <p>Scrap wastes (scrap metals, glass shards, wood pieces, etc.) will be temporarily stored under cover on a solid, leak-proof, safe floor and disposed of by giving them to companies that have an environmental license.</p> <p>Excavation waste will be used for backfill and recycling purposes as much as possible and other appropriate reuse options will be evaluated. Excess excavation waste will be transported and disposed of separately by licensed transportation vehicles to the existing licensed excavation waste storage area(s) determined by the relevant official authorities in the district/region.</p>									



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>Temporary waste areas on-site (including excavated soil for foundations) will be placed at least 300 meters away from the stream that passes through the Tatlar Neighbourhood.</p> <p>For fuel replenishment and transfer of other hazardous liquids, safe and impermeable areas ideally located away from residential areas (at least 50 meters from drainage structures and 100 meters from major water bodies) will be used.</p> <p>After the closure of each construction site, all excavation, debris, and waste will be cleared.</p> <p>Records of waste generation and disposal will be maintained.</p> <p>Whenever possible, appropriate and feasible materials will be reused and recycled.</p> <p>Waste Oils will be collected separately at the source, in barrels marked "waste oil" and on a sealed floor (in a hazardous waste storage area).</p> <p>In case waste vegetable oil will be generated within the scope of the project, waste vegetable oils will be temporarily stored in drums/barrels/tanks marked "waste vegetable oil" in an area with a 25 cm thick sealed reinforced concrete floor. Leak pans will be placed under the barrels. It cannot be mixed with foreign substances. An annual contract will be made with environmentally licensed recovery facilities or vegetable waste oil intermediate storage facilities to collect the oils in question, a waste declaration form will be filled and approved, and a copy is kept for five years to be submitted to the authorities when necessary. It will be sent to the facilities by licensed vehicles.</p>									
Stakeholder Engagement and Grievance Mechanism: Construction-related complaints and temporary disruptions to the local community, including	The Stakeholder Engagement Plan (SEP) framework prepared by the Ministry of Environment, Urbanism and Climate Change in accordance with the World Bank Performance Standards will begin to be implemented before the construction activities of the sub-project are initiated. This procedure will continue during the construction activities. Depending on the project activities, the plan		X		Records of disclosed information, SEP, documents/brochures etc. Meeting minutes,		X		PIU Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
applicable property owners	<p>will be revised if necessary.</p> <p>SEP describes the activities focus on establishing effective communication with individuals who may be affected by the contractor and consultant's work. It is also highlighted the importance of maintaining respect for the local environment and community by implementing a program for regular communication within the scope of the SEP.</p> <p>Before the start of the sub-project, a meeting will be held with the stakeholders of the Küçükatlar Neighbourhood who will benefit and/or be affected by the project. Information about the project including the Grievance Redress Mechanism (GRM) will be disclosed and posters, brochures and flyers prepared by the Supervision Consultant will be distributed. At the meeting, people who will be affected by the project will be allowed to express their questions, concerns and opinions, and their questions will be answered by experts.</p> <p>The Contractor will appoint a contact person, Community Liaison Officer (CLO), to establish direct communication with the community, provide them with appropriate information, and be the first person to contact in order to receive and resolve issues of concern from the public. He/she will frequently inform the people living in the vicinity included in the AoI, about activities and measures taken. CLO will oversee the operation of the Grievance Redress Mechanism (GRM), ensuring that concerns are addressed in accordance with World Bank requirements.</p> <p>From the beginning to the end of the project, grievance boxes will be placed both at the construction site and in the living spaces where the project beneficiaries are currently located (tent and container cities, public buildings they frequently use, etc.).</p> <p>The GRM of the project will manage grievances through the use of "opening" and "closing" forms. The names, contact telephone numbers, and email addresses of all field personnel responsible for</p>				<p>attendance lists</p> <p>Stakeholder engagement log</p> <p>Complaints registry log</p> <p>Consultant's monitoring reports,</p> <p>E&S monitoring and audit reports of the Contractor</p>					



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>inspection and management will be displayed on the site notice board.</p> <p>After obtaining planning permission, official contact will be made with the Neighbourhood Mukhtar, who will then inform potential stakeholders affected by the construction of rural homes. This information will include details about relevant Environmental and Social Risk Management tools, as well as specific times that require sensitivity and attention.</p> <p>Outside working hours, site "Security Personnel" will serve as the main point of contact through the telephone number specified by the GRM, accessible 24/7. They will be able to reach the designated person(s) responsible for communication as needed.</p> <p>All employees will sign/agree to "Behaviour Rules" and receive training to manage potential adverse effects related to social cohesion and Sexual Exploitation and Abuse/Sexual Harassment (SEA/SH) risks. - The social experts will provide training on Gender Equality, GBVH, Code of Conduct and GRM to blue and white-collar employees working for the contractor.</p> <p>All complaints and demands will be documented, thoroughly investigated, and responded to promptly with details on the actions taken. The complaints will be recorded by the Contractor and reported to the Consultant and PUB.</p> <p>Public notice boards displaying the contact information of those responsible for communication, including environmental issues, will be placed in Mukhtar's office, mosque and the entrance of the construction site.</p>									
<p>Labour and Working Conditions: Risks associated with the potential influx of labour and the presence of labor camps (housing conditions,</p>	<p>The contractor will be developed a project Labor Management Plan (LMP) and follow the measures outlined in this plan. This plan includes external workers including expected external labour and working conditions.</p> <p>Clear and understandable information and documents regarding employment terms and conditions, including all applicable</p>		X		<p>Visual inspection of control measures Health records Employee</p>	X	X		<p>PIU Contractor (implementation) Supervision Consultant (audit)</p>	<p>Within the cost of construction</p>



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
child labor risks, gender-based violence and harassment, human rights risks, etc.) and other labor issues	<p>collective agreements within the scope of national labor and employment law, are provided to workers.</p> <p>Regular payment to workers is made as required by national law and the project LMP.</p> <p>Workers will be granted adequate weekly rest periods, annual leave, and sick, maternity, and family leave as required by national law and the project LMP.</p> <p>Written notice about contract termination and severance pay details are sent to workers in a timely manner.</p> <p>Workers will be employed based on the principles of equal opportunities and fair treatment, and no discrimination is made in any aspect of the employment relationship.</p> <p>Project employees, including specific worker groups such as women, persons with disabilities, migrant workers, and child laborers, are provided with appropriate protection and assistance measures in accordance with the World Bank's ESS2 under the Environmental and Social Framework (ESF). This process is carried out in line with the project LMP.</p> <p>Workers will be allowed or encouraged to join labor unions, engage in collective bargaining, or participate in alternative mechanisms.</p> <p>No workers under the age of 18, the minimum age, will be employed or engaged in discussions by the Contractor related to this sub-project. Employment records are open for inspection by the Client and/or the Consultant.</p> <p>Forced labor involving any work or service extracted from a person under threat of force or coercion, not voluntarily performed, is not used in connection with this sub-project.</p> <p>The Contractor establishes a Worker Grievance Mechanism (GM) at the construction site to allow workers to voice their concerns. Contact information for the GRM will be provided to workers.</p> <p>All workers will be provided training on their rights under national</p>				<p>records</p> <p>Review the construction employee contracts</p> <p>Training records</p> <p>Records of worker complaints</p> <p>SSI records of all employees</p>					



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>labor and employment laws, as well as their rights concerning the GM during recruitment and before the implementation of work. Information about the GRM will be given during toolbox talks to announce all employees in case of personnel turnover.</p> <p>The Code of Conduct, and Gender-Based Violence and Sexual Harassment (GBVH) will be prepared and shared with project employees during employment. All employees will be obliged to read and this document and comply with the Code of Conduct while working on the project.</p> <p>Entrances and exits to the construction site will be monitored, and unauthorized access to the site is prevented.</p> <p>The Contractor pays particular attention to workers who may have underlying health issues or may be otherwise at risk, ensuring their fitness for work before they commence employment.</p> <p>All workers receive mandatory legal health check reports upon recruitment. The Contractor informs employees about the precautions to be taken against epidemics and contagious diseases. The Contractor will arrange for safe drinking water, adequate toilet facilities, shelter, rest and meal areas for workers. If external labor is needed a Camp Management Plan is prepared to avoid or reduce negative impacts on the community and maintain constructive relationships between local communities and workers' camps; and establish standards on worker welfare and living conditions at the camps that provide a healthy, safe and comfortable accommodation and environment. Necessary transportation facilities are provided for the workers.</p> <p>First aid kits containing bandages, antibiotic creams, etc., or medical facilities will be provided by the Contractor. Adequate personnel will be designated and trained to provide first aid in case of medical emergencies.</p>									
Cultural Heritage: A coincidental finding	Cultural or historical sites will not be damaged. Prior to land preparation activities, project staff will be trained on chance-		X		Training records		X		Contractor (implementation)	Within the cost of



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	finding procedures. In case of encountering any cultural heritage/asset during construction works (especially excavation and excavation works), the random finds procedure is applied (see Figure 1). TERRP ESMF Annex-9).				Random finding records				Supervision Consultant (audit)	construction
Biodiversity: Potential risks to flora and fauna due to construction activities and improper waste management	There is no vegetation (shrub or tree) in the selected area that would be affected by construction activities. Regarding the fauna of the subproject area the Contactor will carry out all required procedures and will take the mitigation measures.	X			Tree planting records			X	PIU Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
	Cutting down trees or destroying vegetation will be prohibited outside the construction area. Hunting, fishing, catching wild animals or gathering plants will be prohibited.		X		Visual inspection of control measures	X			Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
Specific to Access Roads										
Specific to Rural Road Construction Works										
General Considerations	Will be obtained permission for road extensions from the Municipality and other relevant authorities. Where road widening cannot be avoided, a full report on the need for the work will be submitted to Koltek before any work is carried out on the access roads. The social and environmental impacts of the work and mitigation measures will be detailed. The road to be used will be specified in the Traffic Management Plan. Damage to Neighbouring properties will be avoided during road construction. Project staff and the supply chain will be trained on the access	X			Approval of the explanatory report by Koltek on behalf of the PIU Training records Records of unexpected impacts during the expansion of access routes Correspondence of the			Contractor (implementation) Supervision Consultant (audit) Once during design	PIU	



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>roads to be used.</p> <p>Avoid road construction on unstable soils, steep slopes and nearby stream banks. Where no alternative road alignments are available, additional measures will be implemented (see slope protection section below).</p>				municipality and other authorities Design approval					
	<p>Placement of all construction waste (including earth cuts) to approved disposal sites (at >300 m from streams,) will be controlled.</p> <p>Erosion control measures will be implemented before the rainy season begins, preferably immediately following construction. The measures will be maintained and reapplied until vegetation is successfully established.</p> <p>Sediment control structures will be applied where needed to slow or redirect runoff and trap sediment until vegetation will be established.</p>		X		Visual inspection of control measures	X			Contractor (implementation) Supervision Consultant (supervision)	Included in the cost of construction
Slope protection	<p>The slopes will be protected from erosion and landslides by taking the following measures:</p> <ul style="list-style-type: none"> Indigenous Species, fast-growing grass on slopes prone to erosion. These grasses help stabilize the slope and protect soil from erosion by rain and runoff. Locally available species possessing the properties of good growth, dense ground cover and deep root will be used for stabilization. Provide interceptor ditch, particularly effective in areas of high-intensity rainfall and where slopes are exposed. This type of ditch intercepts and carries surface run-off away from erodible areas and slopes before reaching the steeper slopes, thus reducing the potential surface erosion. On steep slopes, it is planned to use a stepped embankment 		X		Visual inspection of control measures	X			Contractor (implementation) Supervision Consultant (supervision)	Included in the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>(terracing) for greater stability.</p> <ul style="list-style-type: none"> Place a retaining wall at the lower part of the unstable slope. The wall needs to have weeping holes for drainage of the road sub-base, thus reducing pressure on the wall. Rocks (riprap) can be used in addition to protect the slope. Prevent the uncontrolled run-off of water from the road surface with drainage ditches of sufficient size and divert the water away from the downhill slope. 									
Special for Wastewater Systems										
General Considerations for Septic Tanks (If used by the Contractor during construction and in the treatment of Küçüktaşlar's wastewater)	<p>Septic tanks will be had a vent pipe to prevent gas from accumulating inside the reservoir and have a 'manhole' that allows access to the inside of the tank when needed. It will be ensured that the septic tanks have two chambers: the first chamber is for settling sludge, and the second chamber is for aerobic treatment. These chambers will generally treat wastewater better. Partially treated septic tank effluent can pollute groundwater and surface water. In cases where this is not possible, septic tanks will be impervious and designed in accordance with the "Regulation on Opening Pits in Places Where Sewage System Construction Cannot Be Applied" published in the Official Gazette dated 19/03/1971 and numbered 13783 and septic tanks will be sealed.</p>	X			Design approval	Once during design			PIU Contractor (implementation) Supervision Consultant (audit)	Within the cost of construction
	<p>Septic waste will not discharged into an open sewer or other surface waters.</p> <p>Wastewater will be treated before final disposal.</p> <p>This can be achieved through (i) an underground infiltration area, (ii) a vegetated infiltration area, or (iii) a pit for percolation. In</p>		X	X	Wastewater disposal records (if applicable) Protocol with the municipality Records of community awareness		X		Contractor (implementation) Supervision Consultant (audit) Local government (Mukhtar)	Within the cost of construction



Potential Risks and Impacts	Recommended Mitigation Measures	Phase			Monitoring Indicators	Monitoring Frequency			Responsibility for Implementation and Monitoring Planning	Estimated Cost Construction
		Planning	Construction	Operation Phase		Continuous	Monthly	Quarterly		
	<p>cases where this is not possible, septic waste will be periodically removed with vacuum tankers and disposed of within the framework of a protocol established with the relevant municipality having a licensed wastewater treatment facility.</p> <p>The septic tank's volume will be adequately determined to include the quantity of wastewater until it is conveyed to the municipal system (The septic tank volumes will be calculated, evaluated, and submitted for approval to Koltek along with estimated and planning figures before the installation of septic tanks.) The community to ensure the proper will be continued operation of septic tanks as evidence of preventing soil/water pollution should raise community awareness about the periodic inspection of septic tanks. Septic tanks will be regularly disinfected with insecticides to prevent pests and flies.</p>				activities Records of complaints					

7. REPORTING STRUCTURE

The Contractor shall be responsible for recording, reporting, and analyzing the performance regarding the E&S aspects of the sub-project activities. There shall be a transparent record system presenting the monitoring indicators specified in Table 3 Environmental and Social Management Plan. The Contractor's Environmental and Social Management Plan (C-ESMP) shall be submitted before the commencement of construction works and no construction activity under the sub-project shall be undertaken until it is approved. The C-ESMP shall encompass at least the following site-specific management plans; Occupational Health and Safety (OHS) Plan incorporating a Risk Assessment Report and Emergency Response Plan, Community Health, Safety and Traffic Management Plan, Waste Management Plan, Pollution Prevention Plan, Water Supply and Wastewater Management Plan, Labour Management Plan with a procedure as needed. These documents shall be prepared by the contractor, reviewed by Koltek, and approved by PIU.

It is advisable for the Contractor to use a checklist for routine checks and inspections. Visual inspections are a fundamental rule for control measures during site operations; however, without keeping records of inspections, an inspection system and ongoing improvement areas cannot be tracked and therefore assessed. The Contractor shall develop a daily checklist presenting the matters reported in Table 3 Environmental and Social Management Plan. Alongside the daily checklist, the Contractor should utilize weekly, bi-weekly, and monthly checklists as evidence of their review concerning issues requiring inspection at different frequencies; for instance, planning inspection frequencies such as weekly for temporary waste storage areas and hazardous material storage areas, bi-weekly for accommodations unit and kitchen inspections. It is the responsibility of the Contractor to develop checklists for the periodic inspection of the Contractor's units.

The Contractor will benefit from utilizing certain tracking lists to monitor discrepancies identified during internal audits and to monitor incidents and accidents. All issues identified as needing improvement will be followed up with proposed preventive/corrective actions. The monitoring system will also include the person responsible for preventive/corrective action and a specified timeframe for completion of the activity. In the case of an incident or accident, records shall be maintained at least in a descriptive manner of the incident/accident (including plans and photographs), type, outcome, condition of the involved person/material, elimination of the incident/accident, root cause analysis and evaluation report, direct and root causes, the unit/ person responsible for preventive/corrective action as identified through the output of the root cause analysis to eliminate the recurrence of the incident/accident, and the time required to complete the identified action. Monitoring is a critical necessity for the Contractor's quality monitoring and improvement system.

The Contractor is obliged to prepare Monthly E&S Progress Reports and submit these reports to Koltek by the third day of each month at the latest.

Koltek will regularly review checklists, tracking lists, and the Contractor's Monthly E&S Progress Reports and the Contractor will be audited accordingly.

Under the supervision contract, Koltek will develop Monthly Progress Reports concerning the implementation progress/status of the ESMP and GRM. Additionally, Koltek will develop Quarterly Reports and a Final Audit Report that will encompass the Contractor's environmental and social performance.



8 ANNEXES

Annex 1 Title Deeds

TAŞINMAZA AİT TAPU KAYDI						
Zemin Tipi	:Ana Tasınmaz	Ada/Parsel	:113 / 2			
Zemin No	:59053996	Yüzölçüm	:321955.89 m ²			
İl/İlçe	:KAHRAMANMARAŞ/AFŞİN	Ana Tap. Nötk	:HAM TOPRAK			
Kurum Adı	:Afşin					
Mah/Köy Adı	:KÜÇÜKTATLAR					
Mevkii	:MARABA					
Cilt/Sayfa No	:5/450					
Kayıt Durum	:Aktif					

MÜLKİYET BİLGİLERİ						
Sistem No	Malik	Elbirligi No	Hisse Pay/Payda	Metrekare	Edimme Sebebi - Tarih - Yev.	Terkin Sebebi - Tarih - Yev.
168259401	MALİYE HAZINESİ	-	1/1	321955.89	Tesis Kadastro-04/12/1998-	

İpotek								
Alacaklı	Müşterekmi?	Borç	Faiz	Derece/Sıra	Süre	Tesis Tarih - Yev.	Borçlu	SDF Hakkı

Raporlayan : Mehmet ÇİHANGİR
Rapor Tarih ve Saat: 08.04.2023 18:42

Annex 2: Photographs



Photo 1: Küçüktatlar Rural Houses Settlement Area Parcel Rural Houses Area (117/4 and 113/2 Parcels)



Photo 2: Küçüktatlar Rural Houses Settlement Area Parcel Rural Houses Area (117/4 and 113/2 Parcels)



Photo 3: Küçükatlar Parcel 113/2 General satellite view of the area



Photo 4: Küçükatlar Parsel 113/2 and 117/4 General satellite view



Photo 5: Surface image of the subproject area




Photo 6: Surface image of the subproject area



Photo 7: Surface image of the subproject area

Annex 3: Project Disclosure



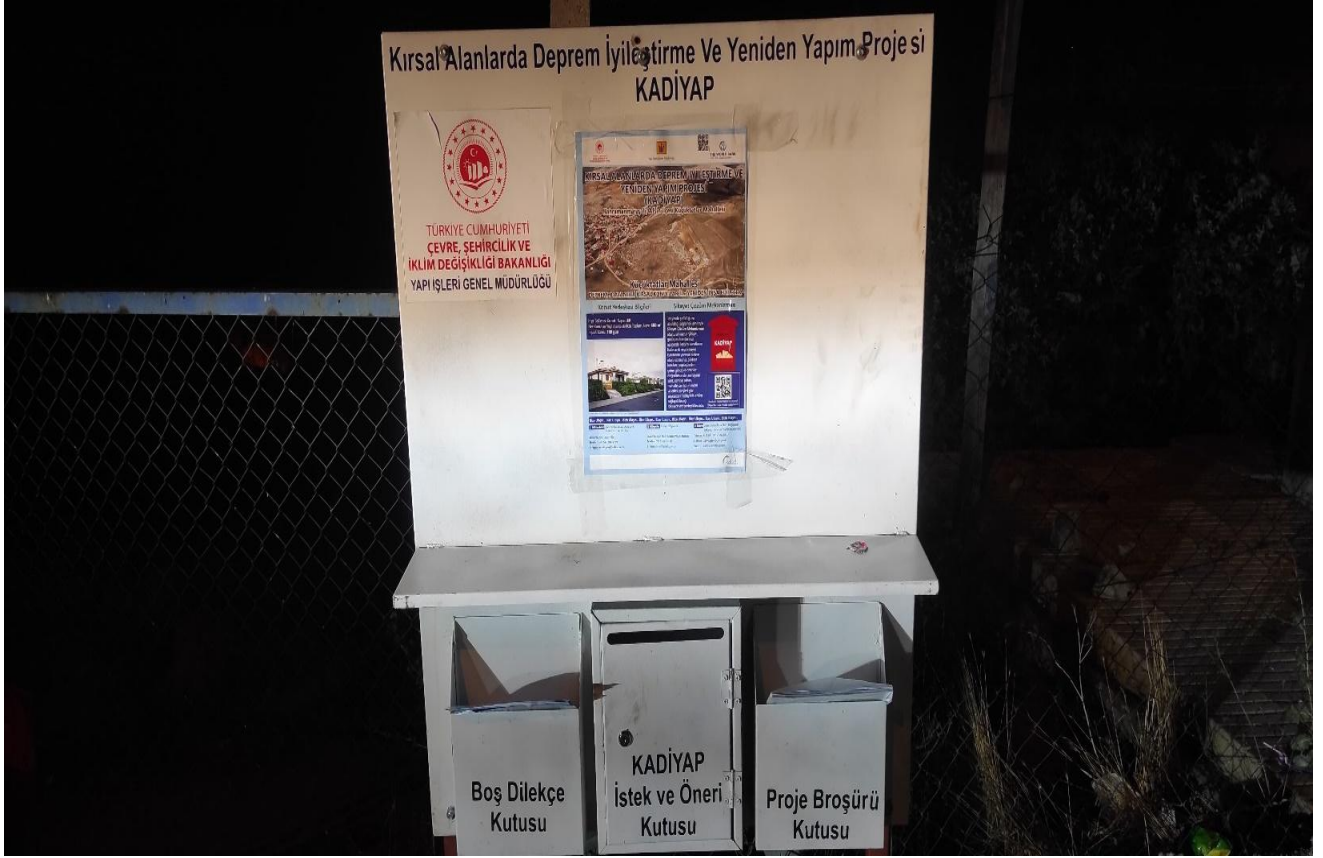

Annex 4 Stakeholder Engagement Meeting Presentation



**KIRSAL ALANLARDA DEPREM İYİLEŞTİRME VE
YENİDEN YAPIM PROJESİ
(KADİYAP)**

**Kahramanmaraş İli Afşin İlçesi Kırsal Konut Projesi
Küçüktatlar Mahallesi**

PAYDAŞ KATILIM TOPLANTISI
30.09.2024
Saat: 14:00



PROJE HAKKINDA

- Proje'nin finansmanı Dünya Bankası tarafından sağlanmakta olup Hazine ve Maliye Bakanlığı garantörlüğünde Çevre, Şehircilik ve İklim Değişikliği Bakanlığı Yapı İşleri Genel Müdürlüğü tarafından yürütülmektedir.
- Proje'nin İnşaat Müşavirliği'ni Koltek Müşavirlik Anonim Şirketi (Koltek) üstlenmektedir.
- Proje kapsamında Kahramanmaraş ilinde Afet ve Acil Durum Yönetimi Başkanlığı tarafından tespit edilen hak sahipleri için belirlenen yeni alanlarda kırsal konutların inşa edilmesi amaçlanmaktadır.

PROJE YÖNETİMİ

Proje Yönetim Birimleri:

BANKA: Finansmanı Sağlayan Kuruluş, *Dünya Bankası*

IDARE: Proje Faaliyetlerin Genel Yönetimi ve Idaresi,
Çevre, Şehircilik ve İklim Değişikliği Bakanlığı,
Yapı İşleri Genel Müdürlüğü (YİGM)


MÜTEAHHİT: İnşaat İşini Yapan Firma, Bulut Yeşil Yapı A.Ş. - AGV Yapı Tic. Ltd. Şti. İş Ortaklığı

MÜŞAVİR: İnşaatı Denetleyen Firma, Koltek Müşavirlik Anonim Şirketi

KADİYAP HAKKINDA


Kırsal Alanlarda Deprem İyileştirme ve Yeniden Yapım
Bileşen 3: Kırsal Konut Yeniden İnşası ve İyileştirilmesi

- Bileşen-3 kapsamında depremden etkilenen diğer iller ile birlikte Kahramanmaraş ilinde belirlenen yerleşimlerde kırsal konutların yeniden inşası bulunmaktadır.
- Bu kapsamda, Soğukpınar Mahallesi'nde AFAD tarafından belirlenen 164 ada ve 24-42 toplam 10 adet konut ve Dukladiroğlu İlçesi Başdervişli Mahallesi'nde 195 ada 14 parselde 86 çelik yapıllı kırsal konut yapımına başlanmıştır.
- İnşa edilen konutlar, hak sahiplerine AFAD tarafından kura ile teslim edilecektir.




KADİYAP Bileşen 3:
Kırsal Konut Yeniden
İnşası ve İyileştirilmesi
Projesi

Küçüktatlar Mahallesi
Kırsal Konutları Vaziyet
Planı:
29 Adet 500 metre kare
parsel alanlı yaklaşık 100
metre kare oturumlu köy
evi yerleşimi.

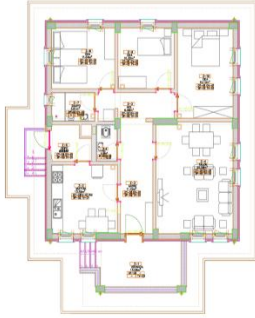


Ev Öğeleri	Büyükük
Oda 1	11,64 m ²
Oda 2	10,32 m ²
Yatak Odası	15,10 m ²
Salon	25,59 m ²
Mutfak	13,59 m ²
Hol	6,08 m ²
Antre	11,15 m ²
WC	2,34 m ²
Banyo	3,61 m ²
Depo	3,97 m ²
Veranda	13,08 m ²
Toplam	116,67 m²

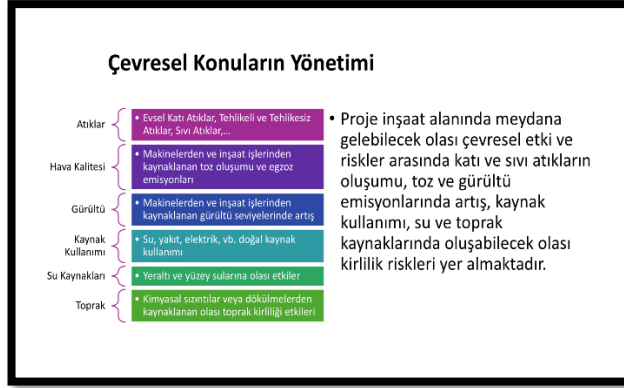


PROJENİN ÇEVRESEL VE SOSYAL DOKÜMANLARI

ÇEVRESEL VE SOSYAL YÖNETİM PLANI (ÇSYP)



- Çevresel ve Sosyal Yönetim Planı (kısaca ÇSYP) olası çevresel ve sosyal etkilerin azaltılabilmesi için ihtiyaç duyulan tedbirlerin yer aldığı, bu etki ve önlemlerin nasıl ve ne şekilde uygulanması ve yönetilmesi gerektiğini ortaya koyan bir plandır.
- Müşavir Firma ile çevresel ve sosyal uzmanlar ÇSYP'nin etkin bir şekilde oluşturulması için 23 Ocak 2024 tarihinde alt proje sahasına ziyarette bulunmuştur.
- Bu saha ziyaretleri kapsamında hem muhtar ile görüşme yapılmış hem de seçilen parselin çevresel ve sosyal değerlendirilmesi yerinde gerçekleştirilmiştir.
- Bu gözlem ve görüşmeler neticesinde Kullar Mahallesi Kırsal Konut İnşaat Projesinin de dahil olduğu bir Çevresel ve Sosyal Yönetim Planı hazırlanmıştır.
- Bu kapsamda öngörülen riskler ve etkilerine göre Çevresel ve Sosyal risk seviyesi «Orta» olarak değerlendirilmiştir.
- Belirlenen çevresel ve sosyal etki ve riskler ÇSYP'de belirtilen önlemlerin uygulanması, tedbirlerin alınması ile çözülebilecektir.

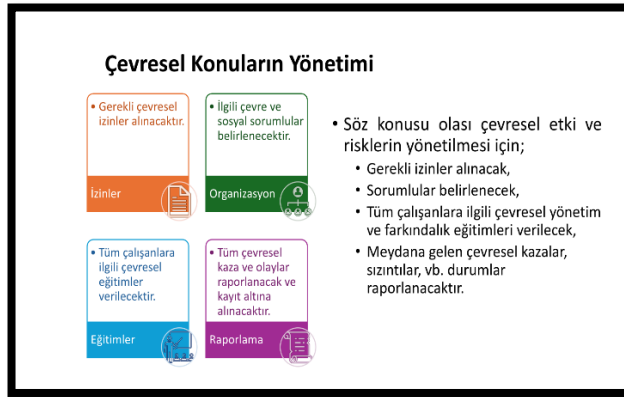

İş Sağlığı ve Güvenliği Yönetimi

- Sorumlular belirlenecektir.
- Tehlikeler tespit edilecek ve risk analizleri gerçekleştirilecektir.
- Tespit edilen risk ve tehlikeler için uygun önlem ve tedbirler değerlendirilecek ve uygulanacaktır.
- Tüm çalışanlara yaptıkları işle ilgili temel düzey ve teknik İş Sağlığı ve Güvenliği (İSG) eğitimleri verilecektir.
- Tüm çalışanların işe giriş muayeneleri işyeri hekimi tarafından yapılacak ve uygunluk raporu düzenlenecektir.
- İnşaat sahası ilgili sorumlular tarafından düzenli olarak denetlenecektir.
- Denetim sırasında tespit edilen uygunsuzluklar rapor edilerek en kısa sürede gerekli aksiyonlar alınacaktır.




İş Sağlığı ve Güvenliği Yönetimi

• Tehlike, risk, önlem, raporlama gibi İSG yönetimine ilişkin adımlara yönelik aşağıdaki örnekler verilebilir.

Tehlike	Risk	Tedbir/Önlem	Eğitim	Tefit ve İz Kontrol	Raporlama
• Yüksekte Çalışma	• Yüksekten düşme sonucu yaralanma	• Yüksekte çalışmaktan kaçınmak, • İlgili Kişisel Koruyucu Donanımları kullanmak.	• Aylık, haftalık, günlük İSG eğitimlere katılmı sağlanmak ve uygulamak	• İlgili sorumlular tarafından düzenli saha turları yapılması, ve kontrol kayıtlarının tutulması	• Günlük, haftalık, aylık raporların düzenlenmesi.


Acil Durum Hazırlık ve Müdahale

- Acil Durum Planının hazırlanması
- Acil Durum Ekiplerinin belirlenmesi ve görevleri ile ilgili eğitimlerin verilmesi
- Acil Toplanma Alanının belirlenmesi ve işaretlenmesi
- Acil Durum müdahale ekipmanlarının tamamlanması ve eksiksiz olması
- Tatbikatlar yapılması
- Tüm çalışanlara acil durumlar hakkında bilgilendirme yapılması



Acil Durum Ekipleri

- Kurtarma
- Koruma
- Söndürme
- İlk Yardım



Toplum Sağlığı ve Güvenliği Yönetimi

Alınacak Önlemler

- İnşaat alanına erişim bariyerlerle ve güvenli personel ile kısıtlanacaktır.
- Saha içerisinde ve yakınında ilgili trafik güvenliği önlemleri alınacak ve uygulanacaktır. Proje sürücülerinin hız limitleri kontrol altında tutulacaktır.
- Makine ve araçların bakımları düzenli olarak yapılacaktır.
- İnşaat ile ilgili bilgilendirmeler yapılacak ve Şikayet Mekanizması etkin bir şekilde uygulanacaktır.

İŞGÜCÜ YÖNETİM PLANI (İYP)



- İYP, projenin inşaat öncesi, inşaat ve işletme aşamalarında geçerli olan, işgücü ve çalışma koşullarına ilişkin gereklilikleri açıklayan bir dokümandır.
- Tüm çalışanlara adil muamele yapılarak eşit fırsatların tanınması ve ayrımcılık yapılmaması için gereken uygulamaları teşvik eder ve uygulamaya koyulmasını sağlar.
- Proje çalışanlarının kendilerinin ve haklarının korunması ve işgücü ile ilgili risklerin yönetilmesi için gerekli altyapının sağlanmasını hedefler.
- İYP, işgücü ve çalışma koşullarına uygunluk, raporlama, roller ve sorumluluklar, izleme ve eğitim açısından gereksinimleri ve beklentileri açıklar.

Paydaş kimdir?

Proje faaliyetlerinden etkilenecek ya da etkilenme ihtimali olan gerçek ya da tüzel kişiler..



- ✓ Kredi veren kuruluşlar
- ✓ Proje sahibi, proje yürütücüsü..
- ✓ Ulusal ve yerel devlet kurum ve kuruluşları
- ✓ Proje alanına yakın yerleşimler
- ✓ Proje kapsamında arazi edinilen PEK'ler.. (Projejenin Etkilenen Kişiler)
- ✓ Dezavantajlı ya da hassas olabilecek PEK'ler (Örneğin; yaşlılar, engelliler, kadınlar, vb.)
- ✓ Sivil Toplum Kuruluşları
- ✓ Üniversiteler, vakıflar, kooperatifler, yerel iş kuruluşları, iş dernekleri, ticaret odaları vs..
- ✓ Yüklenici ve ona bağlı çalışanlar..

Neden Paydaş Katılım Toplantıları Düzenlenir?



- Paydaş katılımı, ilgili proje boyunca gerçekleştirilen kapsayıcı ve süreklilik arz eden bir süreçtir. Doğru şekilde tasarlanıp uygulandığında, projenin çevresel ve sosyal etki ve risklerinin başarılı bir şekilde yönetilmesini ve paydaşlarla sağlam iletişim ve ilişkilerin kurulmasına olanak sağlar.
- Proje sürecinde paydaşlar arasında kurulan erken, sık ve açık iletişim ile olası çatışmalar ve proje gecikmelerinin önüne geçilecektir.



Şikâyet Çözüm Mekanizmasındaki Temel Değerler:

- **Şeffaflık:** Tüm şikâyetler, açık ve anlaşılır bir şekilde şikâyet prosedürü kapsamında değerlendirilir.
- **Tarafsızlık:** Birey veya halk tarafından sunulan her şikâyet veya endişe için adil ve eşit bir şikâyet giderme prosedürü uygulanır.
- **Gizlilik:** Anonim şikâyetler sunulabilir ve çözülebilir. Şikâyet bildirmek kişisel bilgi veya fiziksel varlık gerektirmez.
- **Erişilebilirlik:** Tüm çalışanlar ve paydaşlar kolaylıkla yorum yapabilir veya şikâyetinde bulunabilir.
- **Kültürel Uygunluk:** Yerel halk tarafından dile getirilen bir şikâyet veya sorun, bölgesel kaygılar çerçevesinde değerlendirilir ve oradaki kültürel forma uygun bir çözüm süreci başlatılır.

PROJENİN ÇEVRESEL VE SOSYAL DOKÜMANLARI

Şikâyet Çözüm Mekanizması (ŞÇM)

Şikâyet Çözüm Mekanizması (ŞÇM), herhangi bir paydaşın proje hakkındaki varsa bir şikâyetini iletilmesine veya projenin nasıl planlanacağına, inşa edileceğine ve uygulanacağına dair çözüm yolları sağlayan bir süreçtir.

4982 sayılı Bilgi Edinme Hakkı Kanunu: Herkes kamu kurum ve kuruluşlarının faaliyetleri hakkında bilgi edinme hakkına sahiptir. Bilgi edinme hakkının şeffaflık, eşitlik ve tarafsızlık esaslarına göre uygulanması gerekir.



Şikâyet/Öneri/Talep İletim Kanalları

- **Öneri ve şikâyetlerinizi;** içeriği ne olursa olsun, nasıl kaleme alırsanız bizim için değerli olduğunu bilmenizi isteriz. Genel etik ilkelere uygun olarak yazdığınız öneri ve şikâyetlerinizden dolayı olumsuz herhangi bir durumla karşılaşmayacak ve eleştirilmeyeceksiniz. Öneri ve şikâyetlerinizi farklı yöntemle iletebilirsiniz, *şikâyet kutuları, e-mail, internet formları, yüz yüze ya da telefon ile* iletişiminizi öneri ve şikâyetlerinizin hepsi aynı şekilde değerlendirilir; tarafsız bir kurul tarafından incelenir ve tamamı gizli bilgi statüsündedir.
- Tüm şikâyet iletim kanallarından anonim şekilde (kimlik bilgisi paylaşımadan) öneri/talep ve görüşlerinizi Proje Uygulama Birimine iletebilirsiniz.
- Bu proje hakkında genel bilgi almak, çevresel ve sosyal proje dokümanlarına erişmek ya da öneri ve şikâyetlerinizi bildirmek için; <https://kadiyap.csb.gov.tr/> web sayfasını ziyaret edebilirsiniz.

Şikâyet İletim Kanalları

- Çevre, Şehircilik ve İklim Değişikliği Bakanlığı'nın (ÇŞİDB) hem telefon hem de web sitesi aracılığıyla erişilebilen bir 'Alo181' yardım hattı vardır. Bu yardım hattı aynı zamanda çalışanlar, çözüm ortakları ve daha geniş zümreler için bakanlık düzeyinde bir şikâyet mekanizması işlevi görür. ÇŞİDB tarafından sağlanan tüm çevre ve şehir hizmetleri ile ilgili soru, talep ve şikâyetleri profesyonel olarak yönetilen ALO 181 çağrı merkezi tarafından yanıtlanmaktadır ya da Proje Uygulama Birimine iletilmektedir. 0312 586 48 27 nolu telefondan doğrudan Proje Uygulama Birimine ulaşabilirsiniz.

Çağrı Merkezi : Alo 181
Telefon : 0312 436 34 50
Whatsapp Şikâyet Hattı : +90 532 308 51 19
E-Mail : yigmkadev@csb.gov.tr
Şikâyet Formu : <https://kadiyaponeri.csb.gov.tr/>

Şikâyet İletim Kanalları



İnternet üzerinden şikâyet formuna hemen erişim için lütfen yandaki kodu telefonunuza okutun.



(Bu eylem için akıllı telefonunuzda QR kod uygulaması olmalıdır. Söz konusu uygulama yoksa, herhangi bir internet tarayıcı adres çubuğuna şikâyet formu erişim adresini yazabilirsiniz.)

Şikâyet Kutularının Yeri

Çalışan Personeller İçin;
• Şantiye Alanlarında

Köy Halkı İçin;
• Camilerin Kadın ve Erkek Girişlerinde





SON OLARAK...

Projeyle ilişkin çevresel ve sosyal tüm dokümanlara nereden ulaşılabilir?

- Köy muhtarlığı,
- Proje alanı,
- KADİYAP resmi web sitesi (<https://kadiyap.csb.gov.tr/>)









Annex 5 Stakeholder Engagement Meeting



Annex 6 Project Disclosure Materials

Project brochure


ŞİKAYET ÇÖZÜM MEKANİZMASI

Bize Ulaşın... Bize Ulaşın... Bize Ulaşın...


Müteahhit: Yafa Mühendislik Müşavirlik İnşaat San. ve Tic. A.Ş.
Sorumlu Kişi: Yalçın Çiğ
Telefon: +90 532 308 51 19
E-Posta: email: yoz@yafa.com.tr

Müşavir: Koltek Müşavirlik
Sorumlu Kişi: Elan Arslan (Proje Müdürü)
Telefon: 0312 436 34 50
E-Posta: info@koltek.com.tr

İdare: Çevre, Şehircilik ve İklim Değişikliği Bakanlığı Yapı İşleri Genel Müdürlüğü
Telefon: ALD 181, 0312 586 48 27
E-Posta: yigmakdev@csb.gov.tr
Web: kadiyaponeri.csb.gov.tr




Karekodu telefon/tablet vb okutarak
Şikayet Formuna
anında ulaşabilirsiniz!

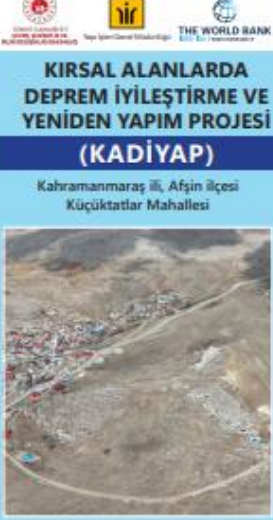

KIRSAL ALANLARDA DEPREM İYİLEŞTİRME VE YENİDEN YAPIM PROJESİ (KADİYAP)

Kahramanmaraş İli, Afşin İlçesi
Küçükatlar Mahallesi




KADİYAP HAKKINDA

KADİYAP Projesi, Türkiye'de 6 Şubat depreminden etkilenen seçilmiş illerde hâlen temel belediye ve sağlık hizmetlerine ve dayanaklı konutlara yeniden erişimini amaçlamaktadır.

Dünya Bankası (DB), Türkiye Deprem İyileştirme ve Yeniden Yapım Projesi'nin (KADİYAP) uygulanmasında Çevre, Şehircilik ve İklim Değişikliği Bakanlığı'nı (ÇŞİDB) desteklemektedir.


Elazığ, Kahramanmaraş, Malatya, ve Adıyaman illerinde yıkılan kiral konutlar altyapıları ile birlikte yeniden inşa edilecektir. Kahramanmaraş İli, Afşin İlçesine bağlı Küçükatlar Mahallesi KADİYAP kapsamında Alt Proje olarak seçilmiştir.



ŞİKAYET ÇÖZÜM MEKANİZMASI

• İletişim ALINAMI	1-112
• İletişim KURULAMAMI	1-155
• İletişim OYUNLAMAMI	1-155
• İletişim için gerekli olanları TAMAMLANMIŞ	1-155
• İletişim için gerekli olanları TAMAMLANMIŞ	1-155
• İletişim için gerekli olanları TAMAMLANMIŞ	1-155

İletişimde şeffaflığı ve sürekliliği sağlamak amacıyla **Şikayet Çözüm Mekanizması** oluşturulmuştur. Şikayet, görüş ve önerilerinizi aşağıdaki iletişim kanallarına kullanarak veya şikayet kutularına yazarak bizlere ulaştırabilirsiniz. Şikayet kutuları, paydaşlardan gelen görüş ve öneriler doğrultusunda konteyner, leet, şantiye sahası, mahalle çarşısının kadın ve erkek girişleri gibi paydaşların kolaylıkla erişim sağlayabileceği lokasyonlara yerleştirilecektir.



Toplam planlanan konut sayısı 29 olarak belirlenmiştir. AFAD tarafından seçilen yerleşim yeri, Çevre, Şehircilik ve İklim Değişikliği Bakanlığı tarafından onaylanmıştır. Yerleşim Planı Koltek Müşavirlik tarafından hazırlanmıştır.

ALT PROJE YERLEŞKESİNDE DEPREME DAYANIKLI 29 KONUT YAPILMASI PLANLANMAKTADIR.

Teslak yerleşim planına göre, her konut 500 m² alan üzerinde 100 m² olarak planlanmış olup, her konutta belirlenmiş bir yeşil alan bulunmaktadır; dolayısıyla her konut biriminin yeşil alanı dâhil toplam alanı 600 m² olarak planlanmıştır.

İnşaat sürecinin planlama/hazırlık aşamasından sonra 180 gün olması beklenmektedir. Yönlendirici firma arazi hazırlama ve inşaat faaliyetlerini yürütmekten sorumludur.

Project Poster

**KIRSAL ALANLARDA DEPREM İYİLEŞTİRME VE
YENİDEN YAPIM PROJESİ
(KADİYAP)**
Kahramanmaraş ili, Afşin ilçesi Küçükttatlar Mahallesi

Küçükttatlar Mahallesi
DEPREME DAYANIKLI KIRSAL KONUTLAR İLE YENİDEN İNŞA EDİLECEK

Konut Yerleşkesi Bilgileri

İnşa Edilecek Konut Sayısı: **29**
Her Konutun Yeşil Alanla Birlikte Toplam Alanı: **600 m²**
İnşaat Süresi: **180 gün**



Şikayet Çözüm Mekanizması

İletişimde şeffaflığı ve sürekliliği sağlamak amacıyla **Şikayet Çözüm Mekanizması** oluşturulmuştur. Şikâyet, görüş ve önerilerinizi aşağıdaki iletişim kanallarını kullanarak veya şikâyet kutularına yazarak bizlere ulaştırabilirsiniz. Şikâyet kutuları; paydaşlardan gelen görüş ve öneriler doğrultusunda konteyner kent, şantiye sahası, mahalle camisinin kadın ve erkek girişleri gibi paydaşların kolaylıkla erişim sağlayabileceği lokasyonlara yerleştirilecektir.





Yüksekde telefon/tablet vb. okunarak Şikâyet Formuna erişim sağlayabilirsiniz!

Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın... Bize Ulaşın...


Müteahhisi: Yafa Mühendislik Müşavirlik İnşaat San. ve Tic. A.Ş.
Sorumlu Kişi: Yalçın Öz
Telefon: +90 532 308 51 19
E-Posta: email: yoz@yafa.com.tr

Müaviri: Koltek Müşavirlik
Sorumlu Kişi: Etan Arslan (Proje Müdürü)
Telefon: 0312 436 34 50
E-Posta: info@koltek.com.tr

İdare: Çevre, Şehircilik ve İklim Değişikliği Bakanlığı Yapı İşleri Genel Müdürlüğü
Telefon: ALD 181, 0312 586 48 27
E-Posta: yigmkadev@csb.gov.tr
Web: kadiyaponeri.csb.gov.tr



Annex 7 Neighborhood Settlement Plan (117/4 and 113/2 Parcels)

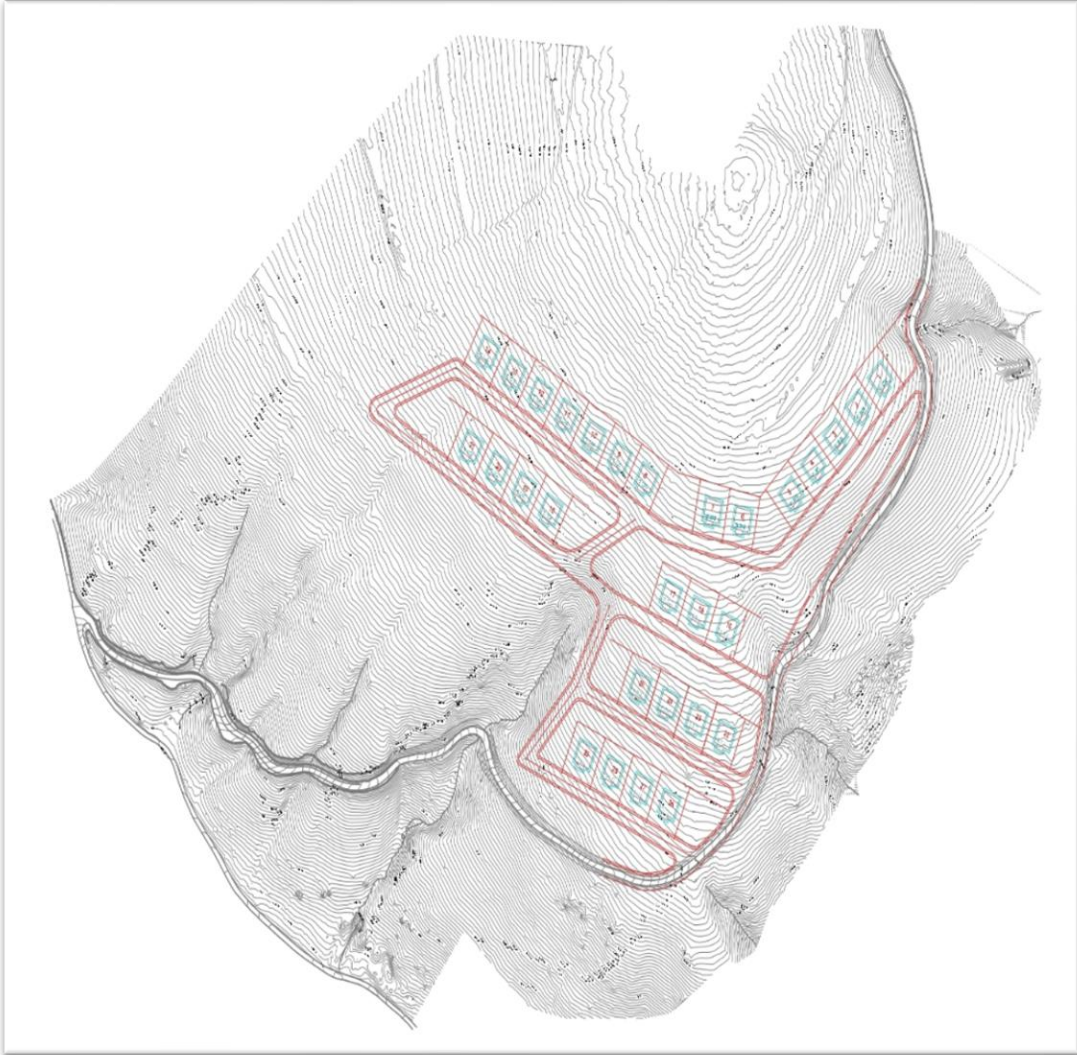

Annex 8: Screening Form (given as a separate document)
